

**DAILY CONSTRUCTION REPORT**

Date: Monday, 08-21-2017  
(Day 84)

**PROJECT:** Middle Road Improvements  
**CLIENT:** Town of Cumberland  
**CONTRACTOR:** Storey Brothers  
**PROJECT MANAGER:** Dan Diffin, P.E.

**WEATHER:** Sunny w/scattered clouds  
**TEMP:** Upper 70s to Mid 80's  
**WIND:** Light breeze  
**HUMIDITY:** Slightly hazy, humid

**FIELD FORCE**

Name of Contractor	Supervisor	Non-Supervisor	Remarks
Storey Brothers	1	3	Installing water line
McGoldrick Brothers Blasting	1	2	Drilling and blasting ledge for water line installation
Fairpoint		1	Shifting service drops
Ace Security		3 Flaggers	1 Flagger at each end of work zone plus "Breaker".

**VISITORS**

Time	Name	Representing	Remarks

**EQUIPMENT**

3 Excavators – CAT 316F, CAT 330D, CAT 329D
2 Smooth Drum Rollers – IR 116D
1 Dozer - CAT D5K2 (idle)
2 Loaders – CAT 930H, CAT 930M
1 FLEXIROC Percussion Rock Drill (idle McGoldrick)

**TODAY'S CONSTRUCTION ACTIVITIES**

Storey Brothers installed approximately 180 lf of water line, STA 49+25 to STA 47+45. New Gate Valve (12") and chlorinating tap installed STA 49+25.
McGoldrick Brothers drilled and blasted ledge ahead of water line installation.
Fairpoint moved some of their service drops to facilitate the transfer of cable company wires onto new poles.

**TOMORROW'S ANTICIPATED CONSTRUCTION ACTIVITIES**

Continue water line installation
Drill and Blast for water main installation

**QUALITY ASSURANCE**

SME on-site to oversee progress, facilitate communications, and inspect erosion control measures.
---


**DISTRIBUTION:**

- 1 SME
- 2 Town of Cumberland
- 3 Storey Brothers, Inc.
- 4 Summit Natural Gas
- 5 Central Maine Power

BY: Jeff Read, P.E.

TITLE: Field Engineer

SEVEE & MAHER ENGINEERS, INC.  
CONSTRUCTION PHOTOS  
August 21, 2017

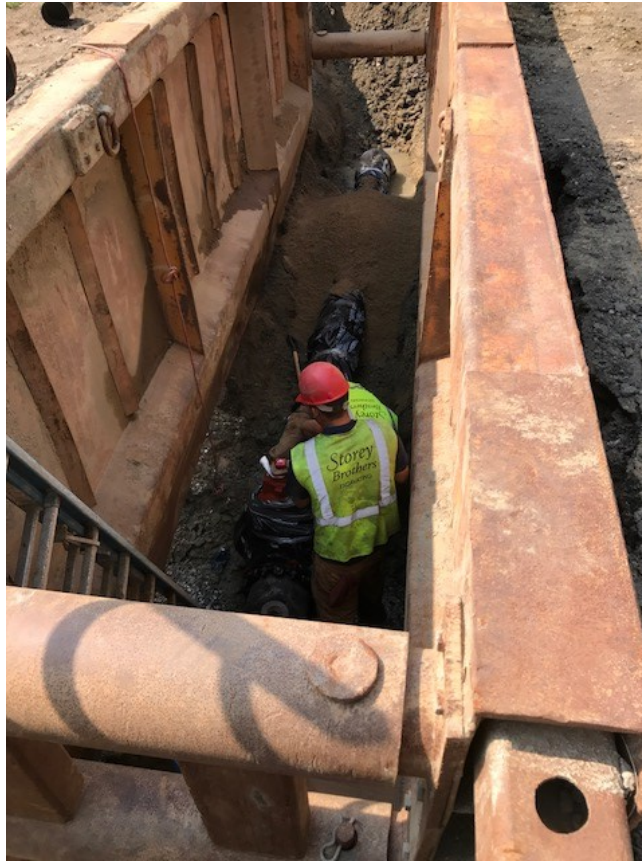

Gate Valve Installation STA 49+25.



Post blast after mat removal STA 34+00.
