



## WEEKLY FIELD OBSERVATION REPORT

Project: Route I Roadway Improvements

Client: Town of Cumberland

GPCEI Project No: 1636.83

GPCEI Field Rep: Asher Anderson (AJA)

Report Date: May 10, 2017

---

### **Work Completed Last Week**

Wed. 5/10/16	Shaw Brother's crew installed reclaimed material as road shoulders in the southbound lane in the middle portion of the project.
Thurs 5/11/17	Shaw Brother's crew installed reclaimed material as road shoulders in the southbound lane in the southern portion of the project.
Fri 5/12/17	Shaw Brother's crew installed reclaimed material as road shoulders in the left lane on the southern portion of the project. Main Line Fence crew installed the guardrail on both sides of the Tuttle Road Ramp. Keenan Excavation crew adjusted manhole covers on the southern portion of the project in the left lane.
Sat 5/13/17	No activity.
Sun 5/14/17	No activity.
Mon 5/15/17	Shaw Brother's crew installed loam and reclaimed material in the road shoulders in the left lane on the southern portion of the project. Coastal Road Repair (CRR) performed 928.39 square yards of Butt Joints and 826.39 square yards of Pavement Surface Removal throughout the project.
Tues 5/16/17	Shaw Brother's crew installed loam and reclaimed material in the road shoulders in the northbound lane on the northern portion of the project.

### **Work Schedule Next Week**

Wed. 5/17/16	No activity.
Thurs 5/18/17	No activity.
Fri 5/19/17	No activity.
Sat 5/20/17	No activity.
Sun 5/21/17	No activity.
Mon 5/22/17	No activity expected. Paving operations are possible.
Tues 5/23/17	No activity expected. Paving operations are possible.

### **Useful Information and Highlights**

- Surface pavement installation date for Route I and the Tuttle Road Ramp is to be determined.

Prepared By: Asher Anderson

Reviewed By: Doug Reynolds

If there are any discrepancies, please notify the sender immediately.



5/10/17 - Installation of reclaim shoulder, looking south



5/10/17 - Installation of reclaim shoulder, looking south



5/11/17 - Installation of reclaim shoulder, looking north



5/12/17 - Installation of reclaim shoulder, looking south




5/12/17 - Guardrail installation on the Tuttle Rd. Ramp



5/15/17 - Installing a butt joint on the north end of the project, looking north



5/15/17 - Installing butt joint on Thomas Drive, looking south

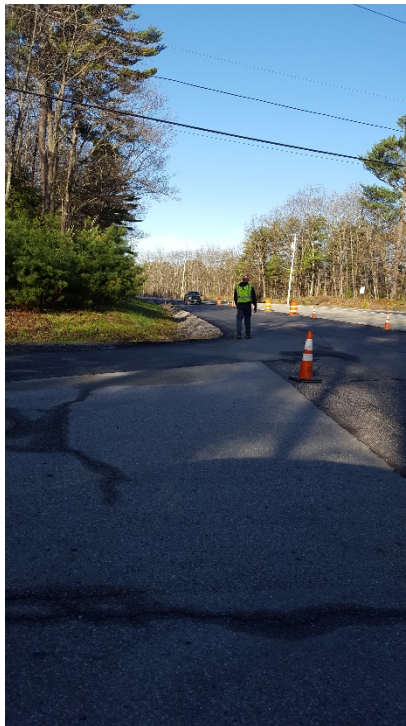

5/16/17 - Area where the crew will work the road shoulders, on Thomas Drive looking south
