

Bayson House Wildwood

Front of House

101.2'

96.5'

Screen
Clean Out

Stake Birch

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 6/30/83

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 2

Connection at Sewer Main WYE, MH35-6'

Occupant _____


Depth, End of Service Pipe 4.5' @ EXISTING SEWER

Owner _____

Length of Service Pipe Laid 48'

Measured, Located By _____

Project Contractor S.E. MACMILLAN

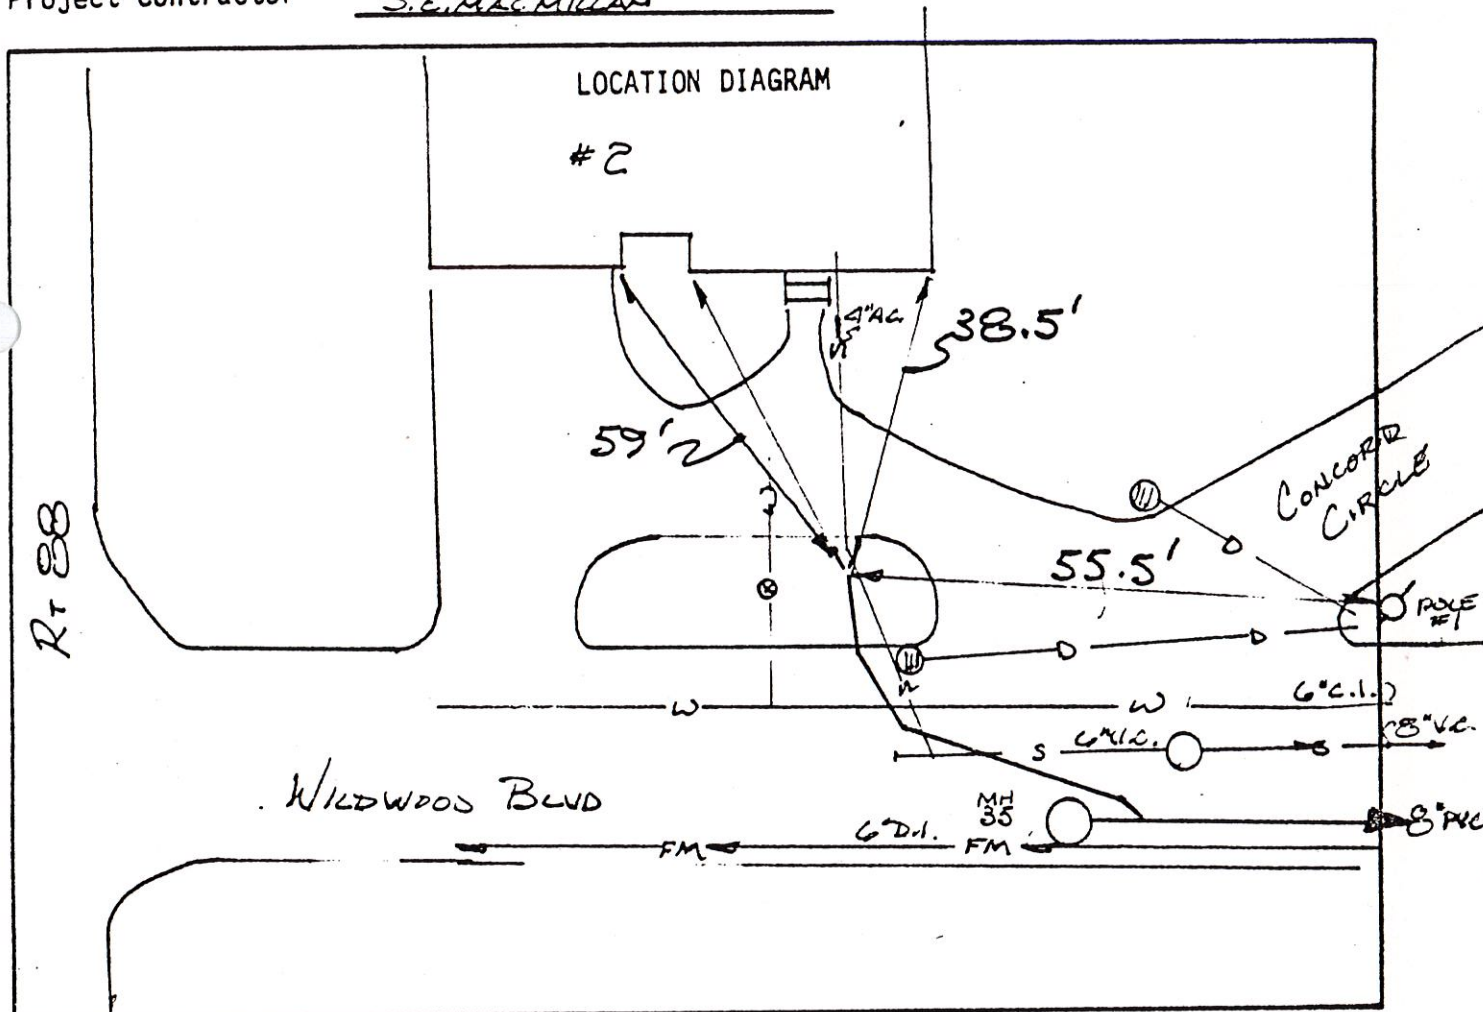

Remarks: 6" PVC GOES UNDER 6" V.C. BY 6" UNDER WATER MAIN
BY 1". NEED 6" X 9" REDUCER & 22° BEND TO CONNECT.

SANITARY SEWER SERVICE LOCATION

Town, City of: Cumberland

Installed 6-21-83

Street Wildwood Blvd.

Type, Size of Service Pipe 6" PVC

Dwelling No. #5

Connection at Sewer Main TEE

Occupant _____

Depth, End of Service Pipe 5.0'

Owner _____


Length of Service Pipe Laid 17.0'

Measured, Located By _____

Project Contractor S. E. MacMillan

LOCATION DIAGRAM


Wildwood Blvd.

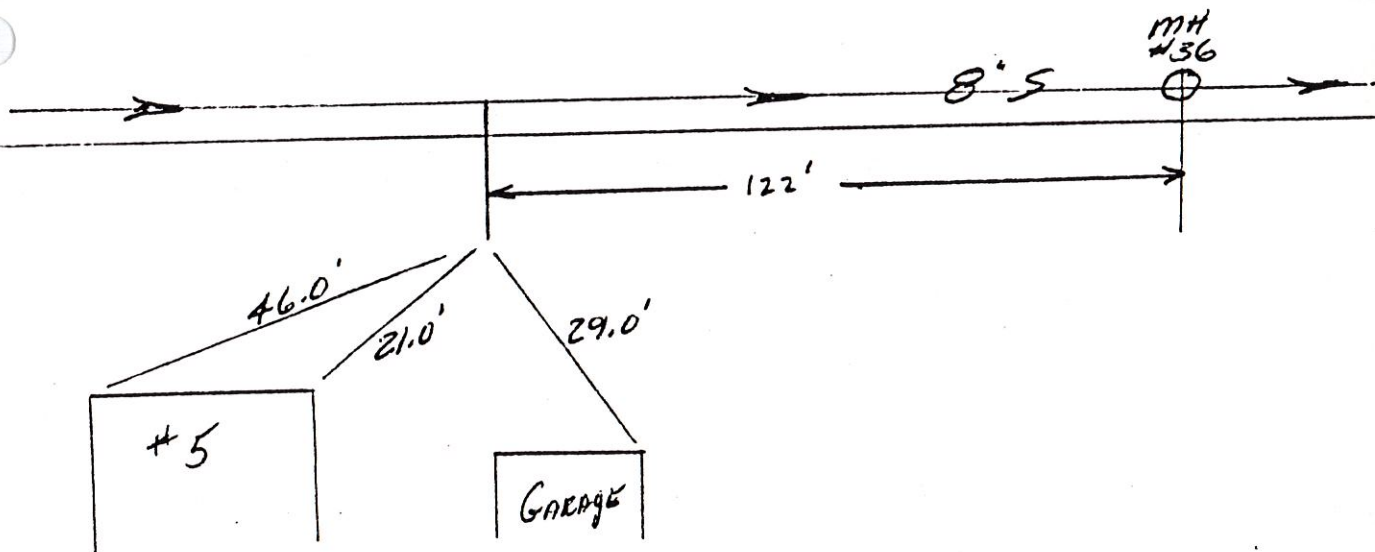

Remarks:


4" outside
3" inside

SAMPLE BUILDING SEWER SKETCH

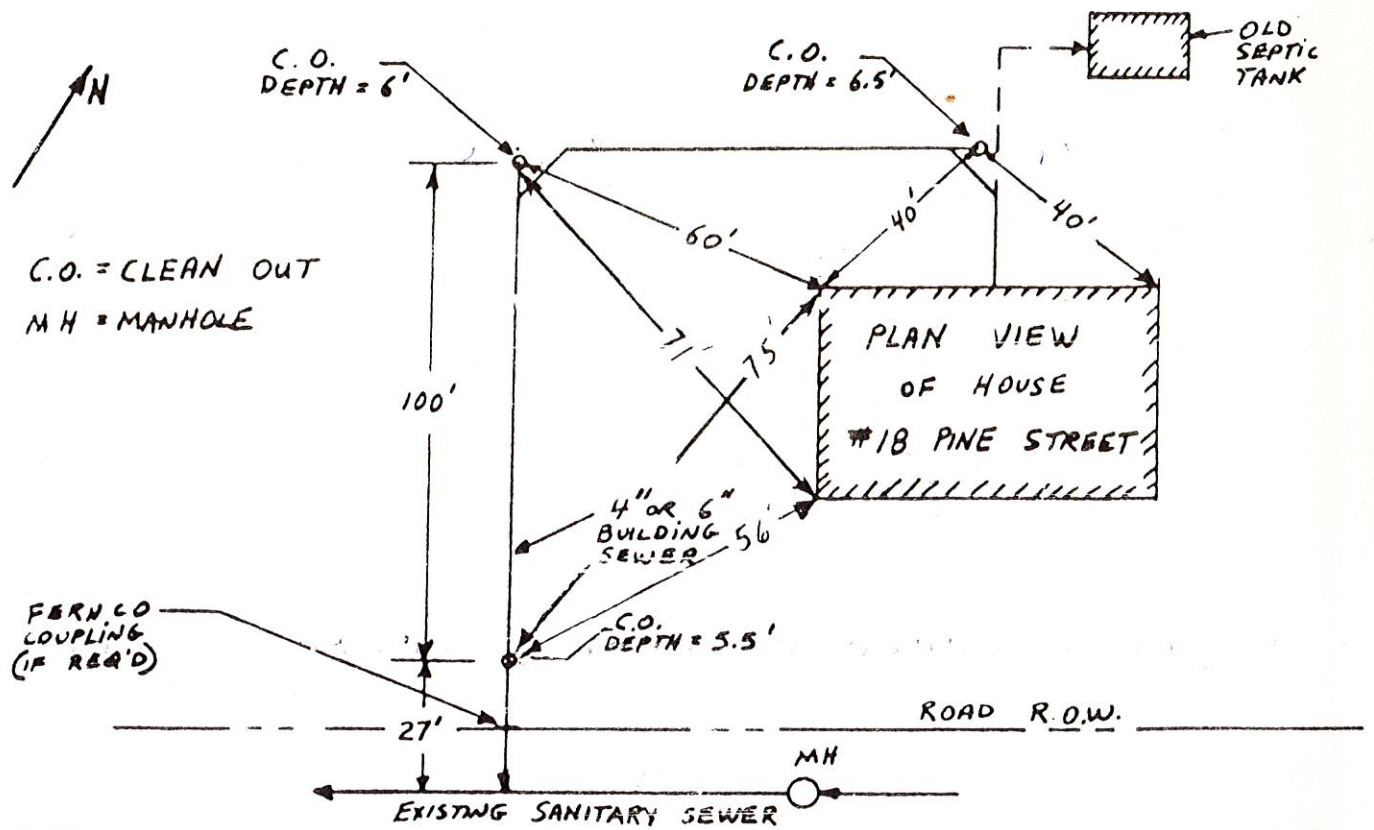

NAME: Laura Young
ADDRESS: 5 Wildwood
CONTRACTOR: Scott Dugan

DATE: 6-15-84
COLLECTOR OR INTERCEPTOR

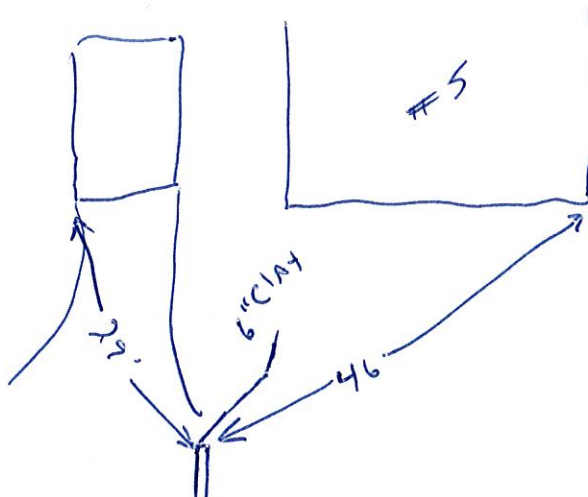

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed JUNE 29, 1983

Street WILDWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 6

Connection at Sewer Main WYE

Occupant _____


Depth, End of Service Pipe 3'

Owner _____

Length of Service Pipe Laid 25'

Measured, Located By _____

Project Contractor S.E. MACMILLAN

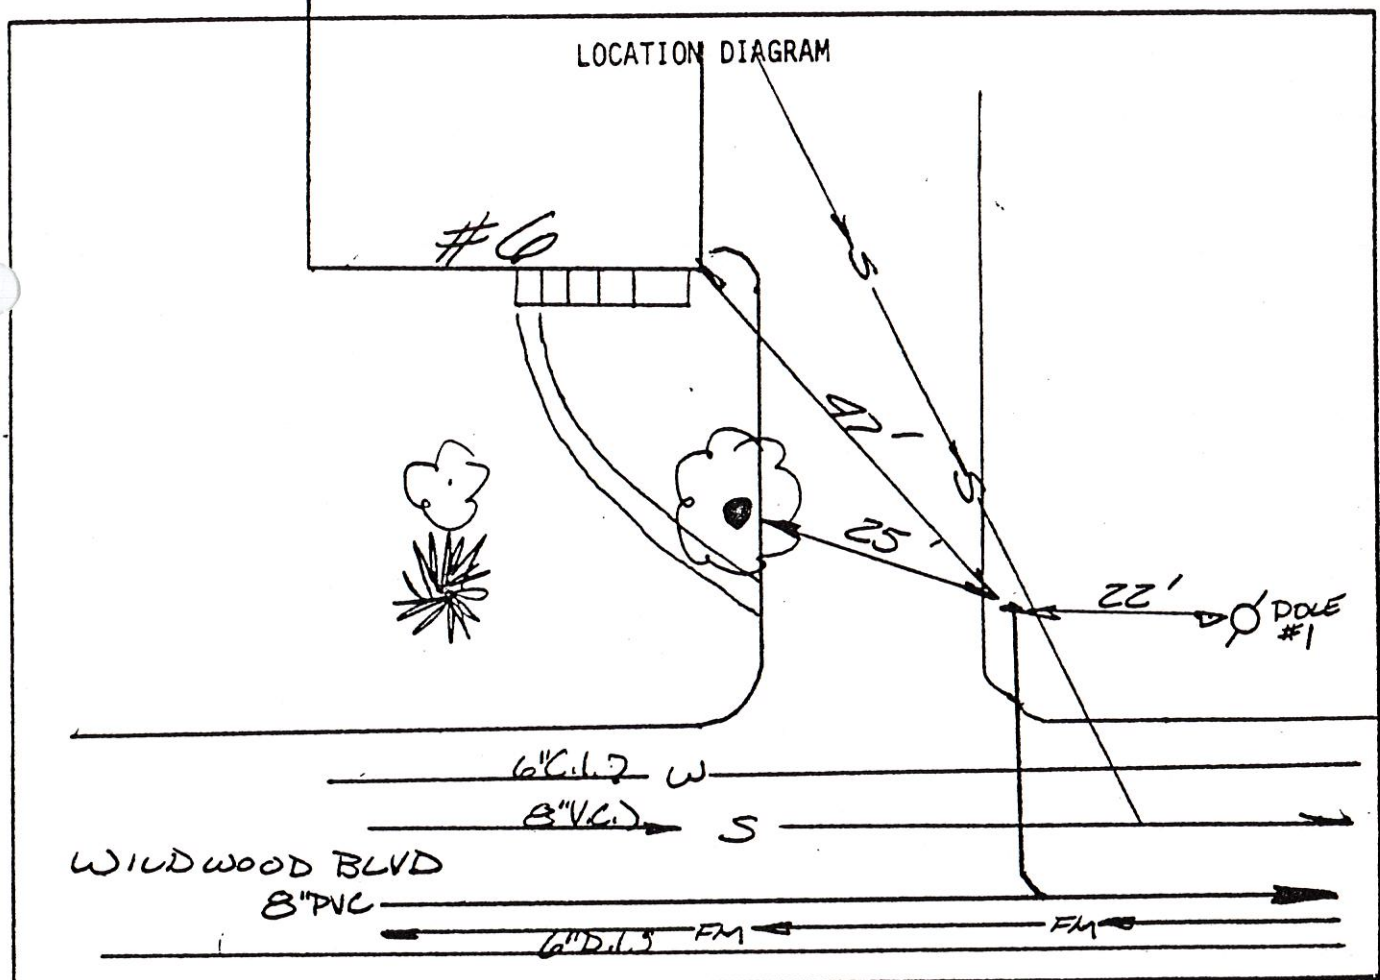

Remarks: 6" PVC BROUGHT TO SIDE OF EXISTING 9" CAST IRON
SEWER.

6" PVC GOES UNDER 8" V.C. & 6" C.I.

SANITARY SEWER SERVICE LOCATION

Town, City of: Cumberland

Installed 6-21-83

Street Wildwood Blvd.

Type, Size of Service Pipe 6" PVC

Dwelling No. #7

Connection at Sewer Main TEE

Occupant _____

Depth, End of Service Pipe 5.5'

Owner _____

Length of Service Pipe Laid 13.0'

Measured, Located By _____

Project Contractor S.E. MacMillan

LOCATION DIAGRAM

Wildwood Blvd.

8' S

MH
#36

24'

76.5'


47.5'

36.0'

#7


Remarks:

SAMPLE BUILDING SEWER SKETCH

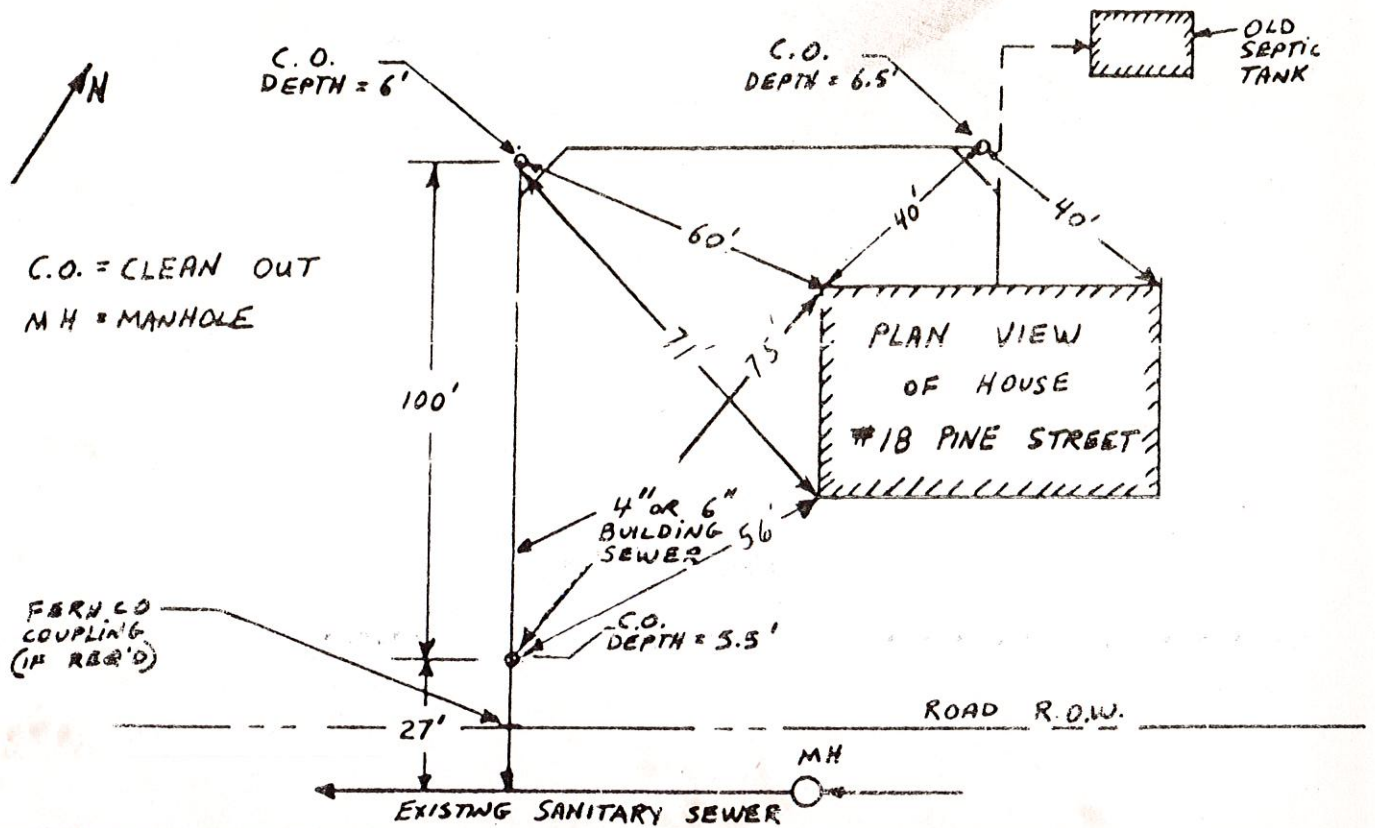

NAME: Gordon Erickson
 ADDRESS: 7 Wildwood
 CONTRACTOR: Scott Dugas

DATE: 6-15-84
 COLLECTOR OR INTERCEPTOR

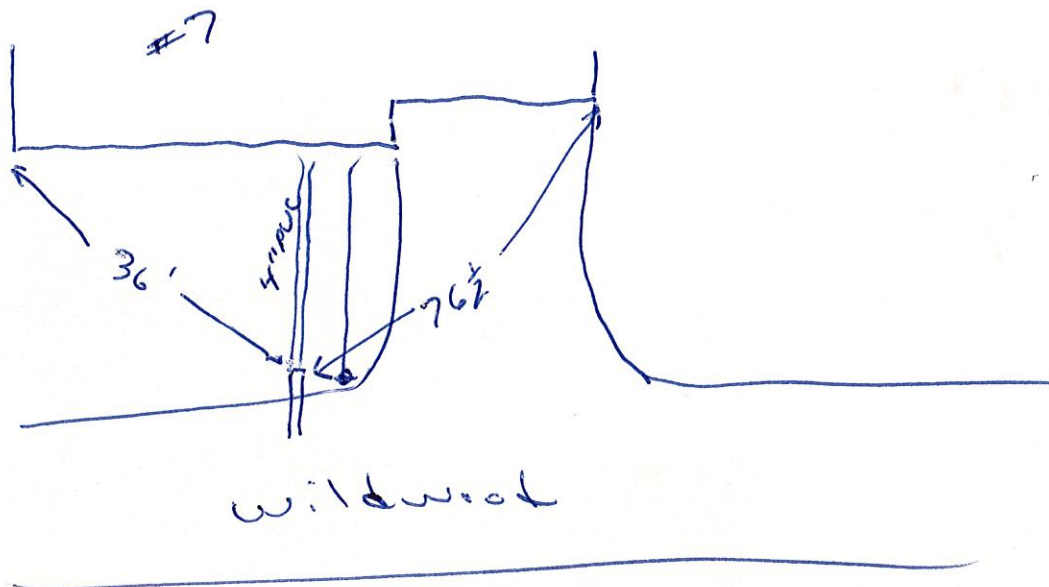

SANITARY SEWER SERVICE LOCATION

Town, City of: Cumberland

Installed 6-24-83

Type, Size of Service Pipe 6" PVC

Connection at Sewer Main TEE

Depth, End of Service Pipe 5.5'

Length of Service Pipe Laid 33.5'

Measured, Located By _____

Street Wildwood Blvd.


Dwelling No. # 8

Occupant _____

Owner _____

Project Contractor S.E. Mac Millan

LOCATION DIAGRAM

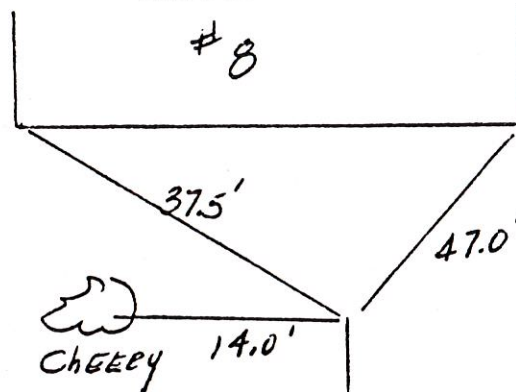

Remarks:

SANITARY SEWER SERVICE LOCATION

Town, City of: Cumberland

Installed 6-20-83

Street Wildwood Blvd.

Type, Size of Service Pipe 6" PVC

Dwelling No. # 9

Connection at Sewer Main TEE

Occupant _____

Depth, End of Service Pipe 5'-0


Owner _____

Length of Service Pipe Laid 18.5'

Measured, Located By _____

Project Contractor S E MacMillan

LOCATION DIAGRAM

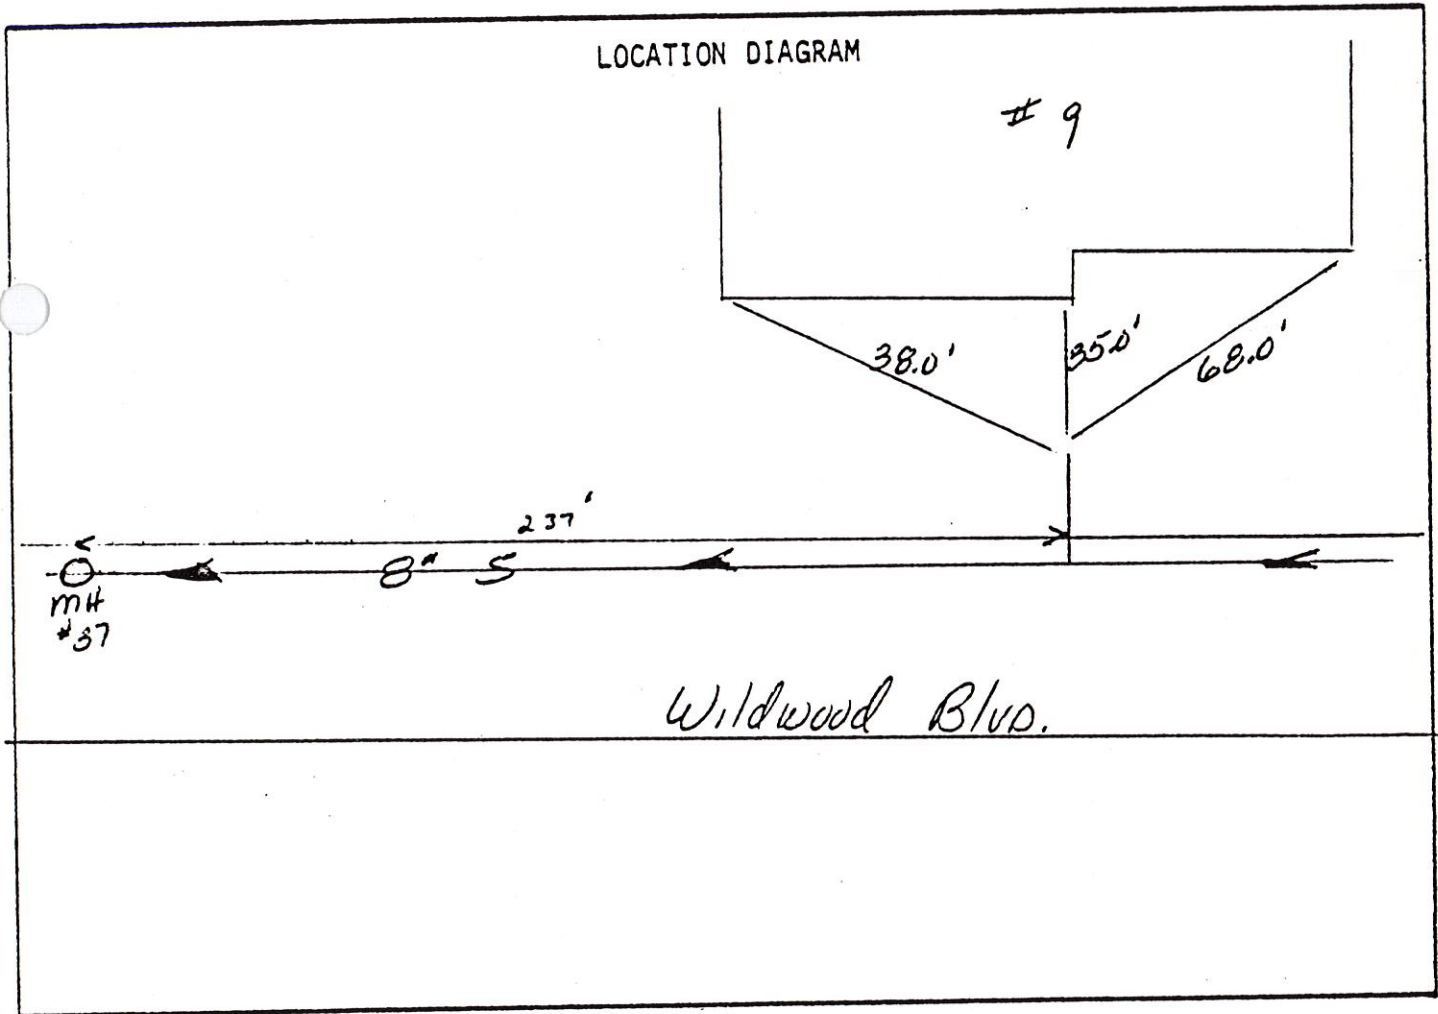

Wildwood Blvd.

Remarks:

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed JUNE 29, 1983

Street WILDWOOD

Type, Size of Service Pipe 6" PVC

Dwelling No. 10

Connection at Sewer Main WYE

Occupant _____


Depth, End of Service Pipe 4.5'

Owner _____

Length of Service Pipe Laid 42'


Measured, Located By _____

Project Contractor S.E. MACMILLAN

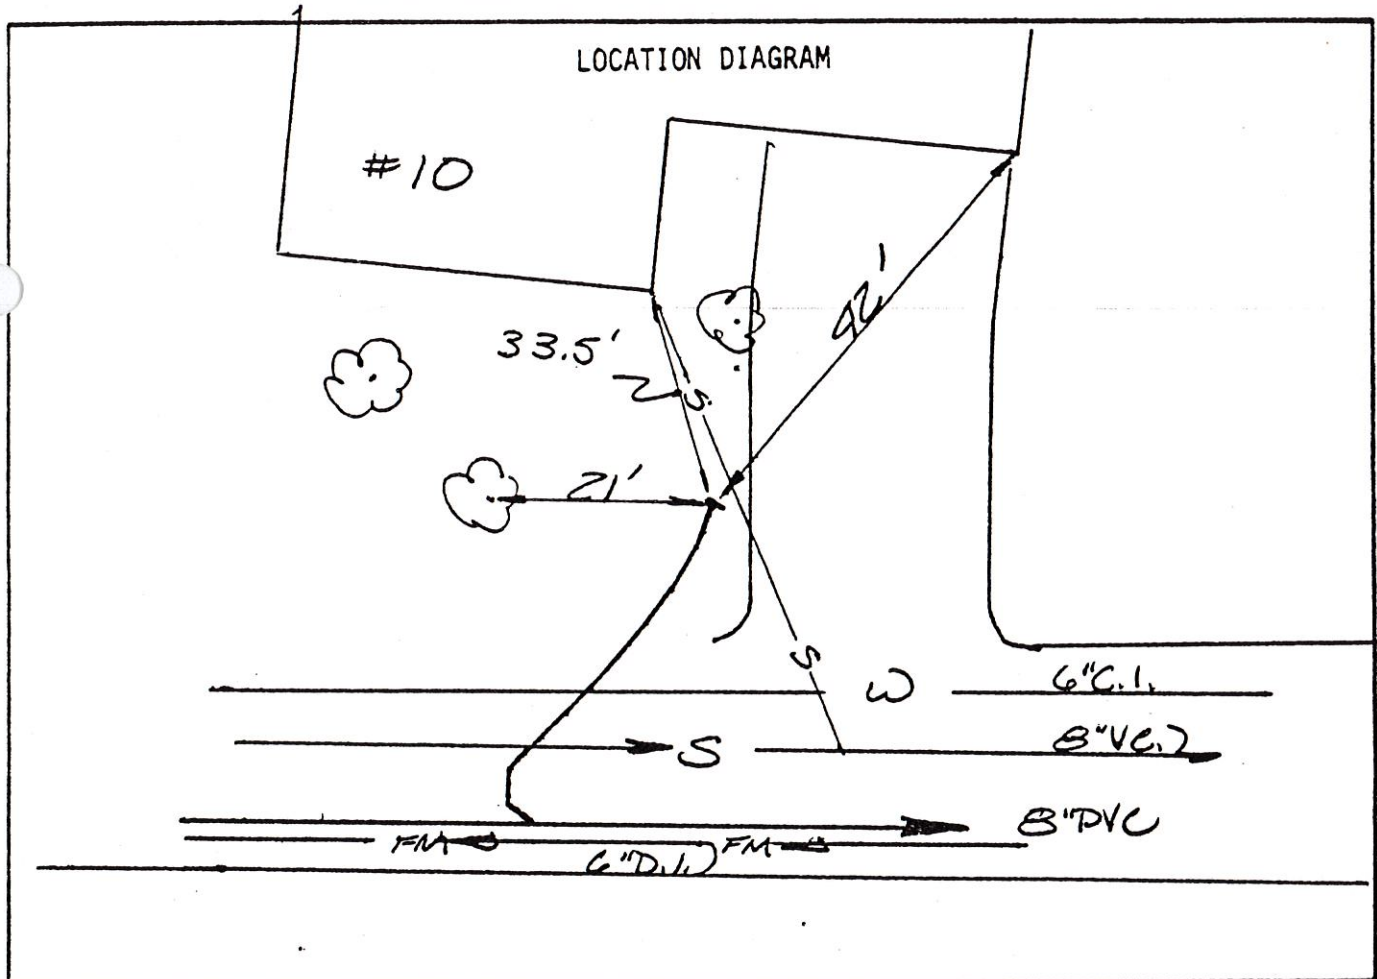

Remarks: 6" PVC GOES UNDER 8" V.C. & 6" C.I. - BROUGHT TO RE
& BESIDE EXISTING 9" A.C. SEWER

SAMPLE BUILDING SEWER SKETCH

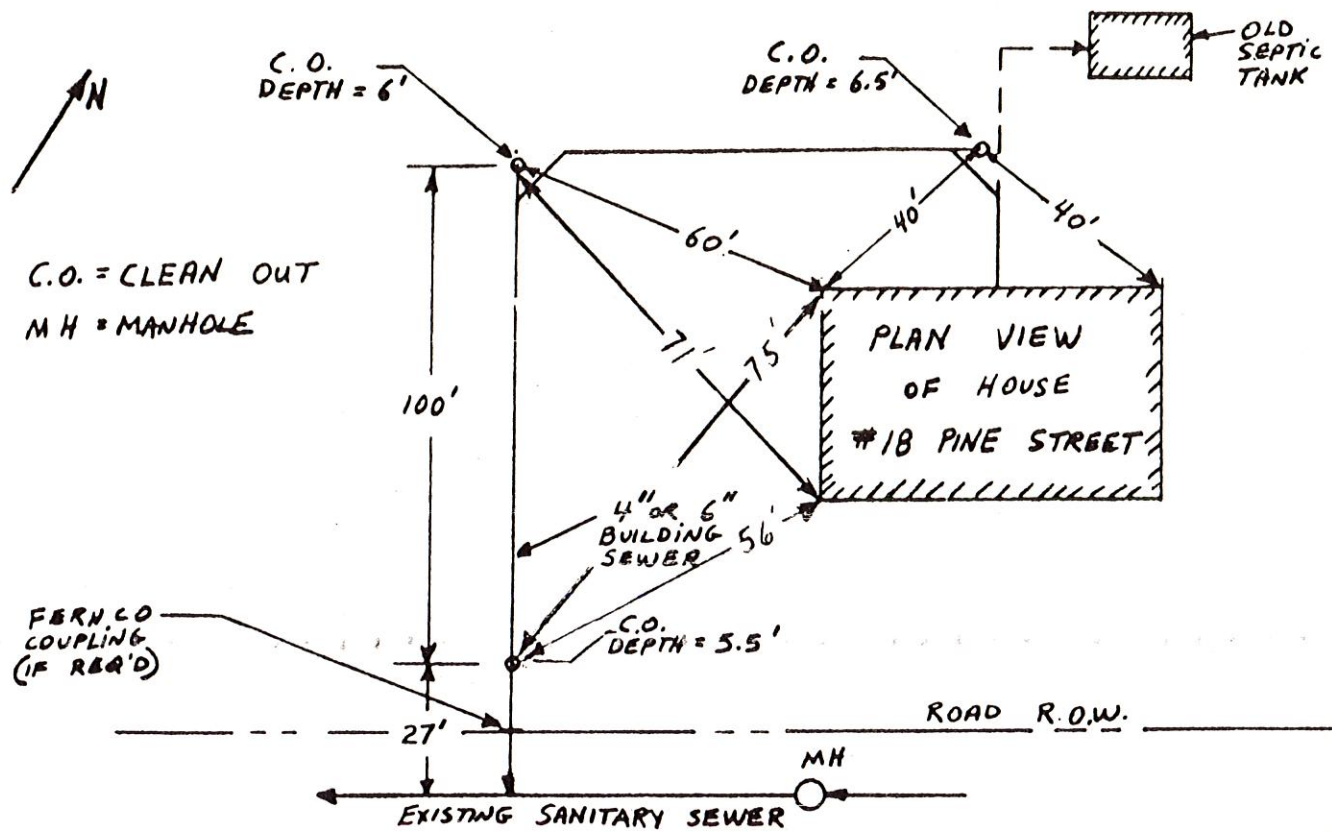


NAME: John Keyser

ADDRESS: 10 Wildwood

CONTRACTOR: Scott Dugan

DATE: 7-10-84

COLLECTOR OR INTERCEPT

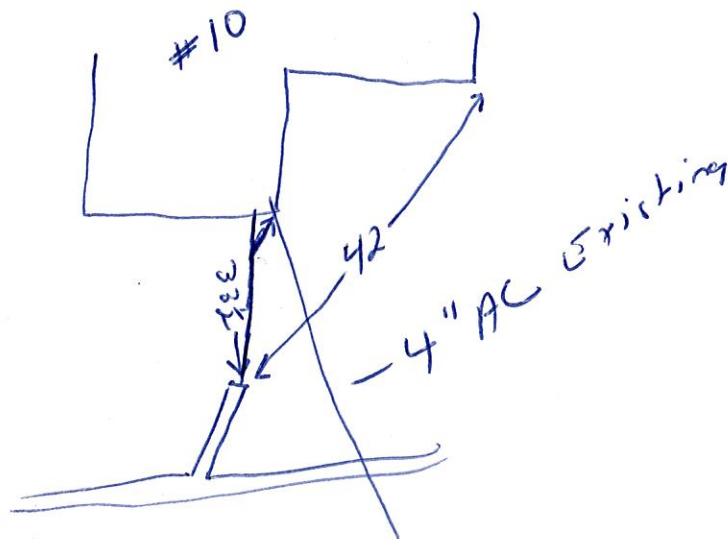

Town, City of: CumberlandDate Installed 6-20-83Street WildwoodType, Size of Service Pipe 6" PVCDwelling No. # 11Connection at Sewer Main TEE

Occupant _____

Depth, End of Service Pipe 6.0'


Owner _____

Length of Service Pipe Laid 19.5'

Measured, Located By _____


Project Contractor _____

LOCATION DIAGRAM

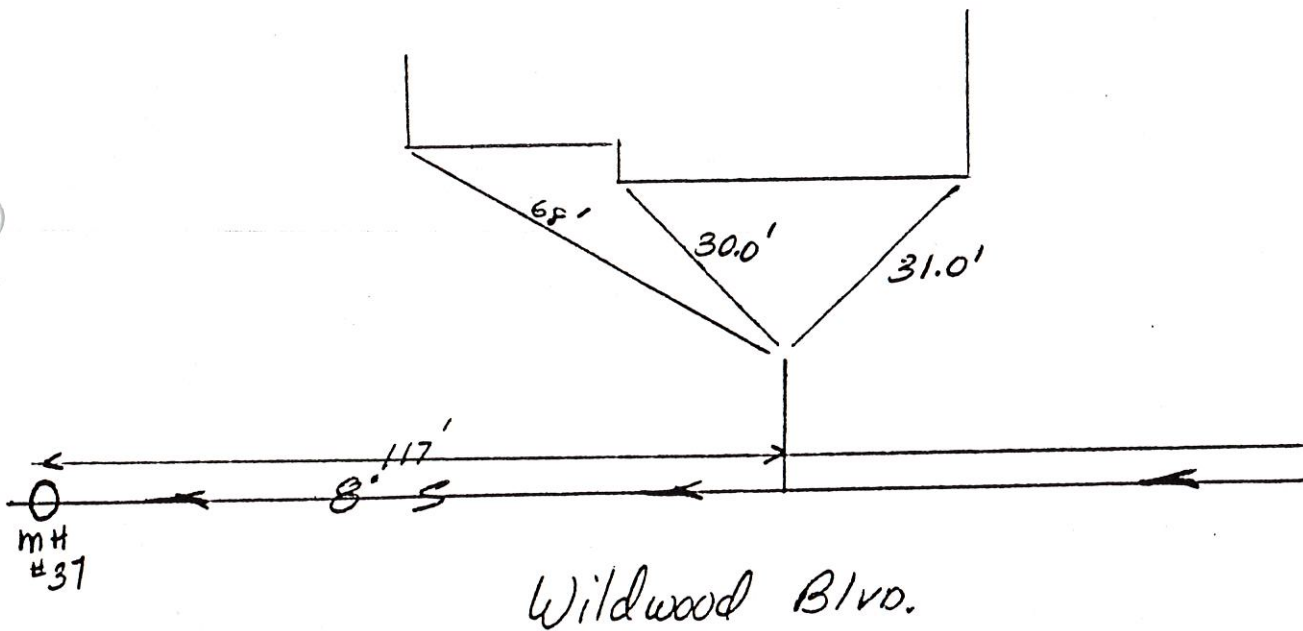


Remarks:

SAMPLE BUILDING SEWER SKETCH

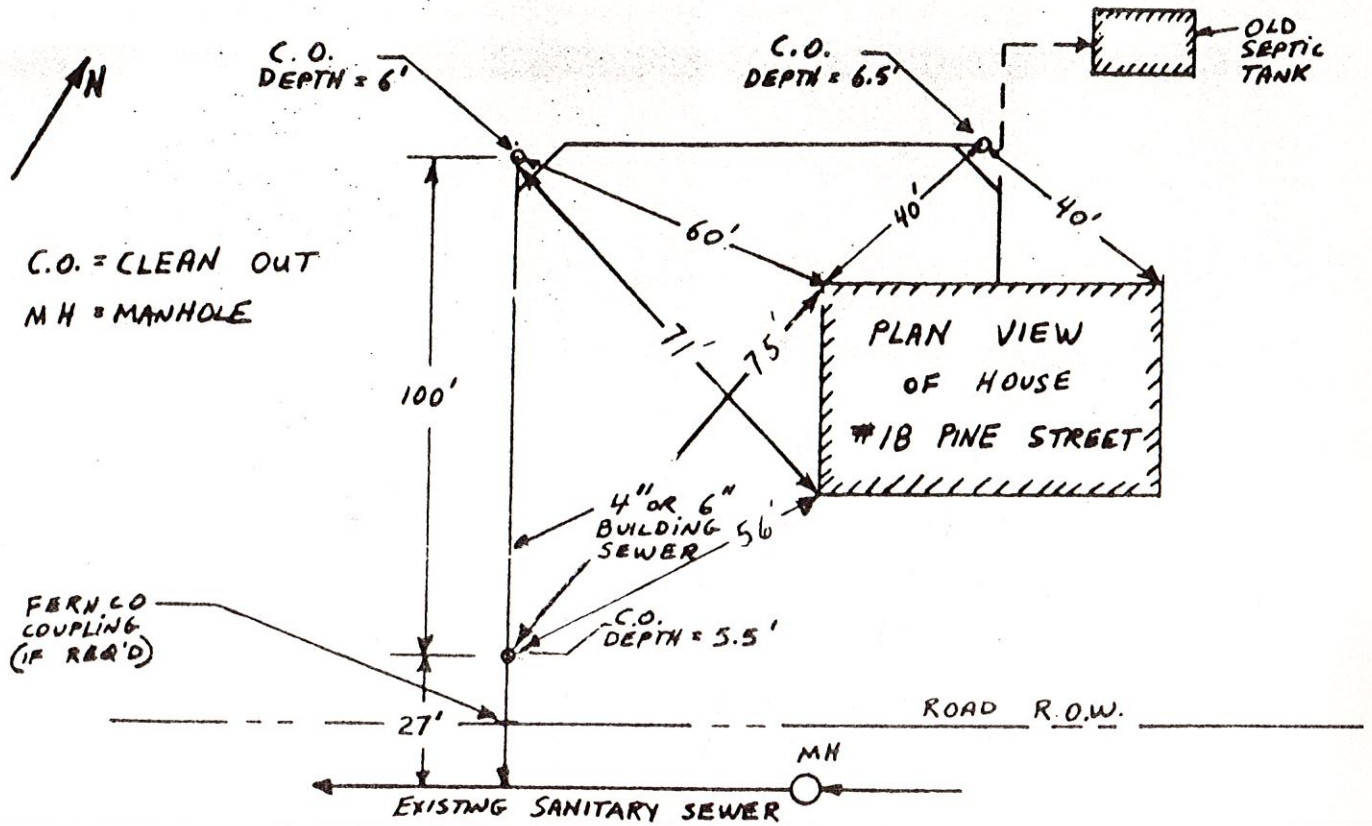

NAME: Bill Courtland
 ADDRESS: 11 Wildwood
 CONTRACTOR: Scott Dugan

DATE: 6-15-84
 COLLECTOR OR INTERCEPT

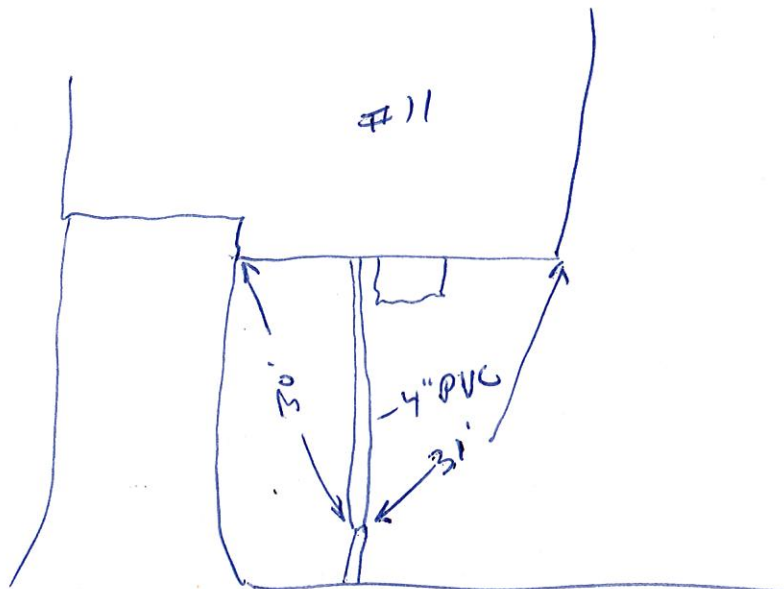

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 6/28/83 7/27/83

Street WILDWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 12

Connection at Sewer Main WYE

Occupant _____


Depth, End of Service Pipe 6' @ EXISTING SEWER

Owner _____

Length of Service Pipe Laid 52.5'


Measured, Located By _____

Project Contractor S.E. MACMILLAN

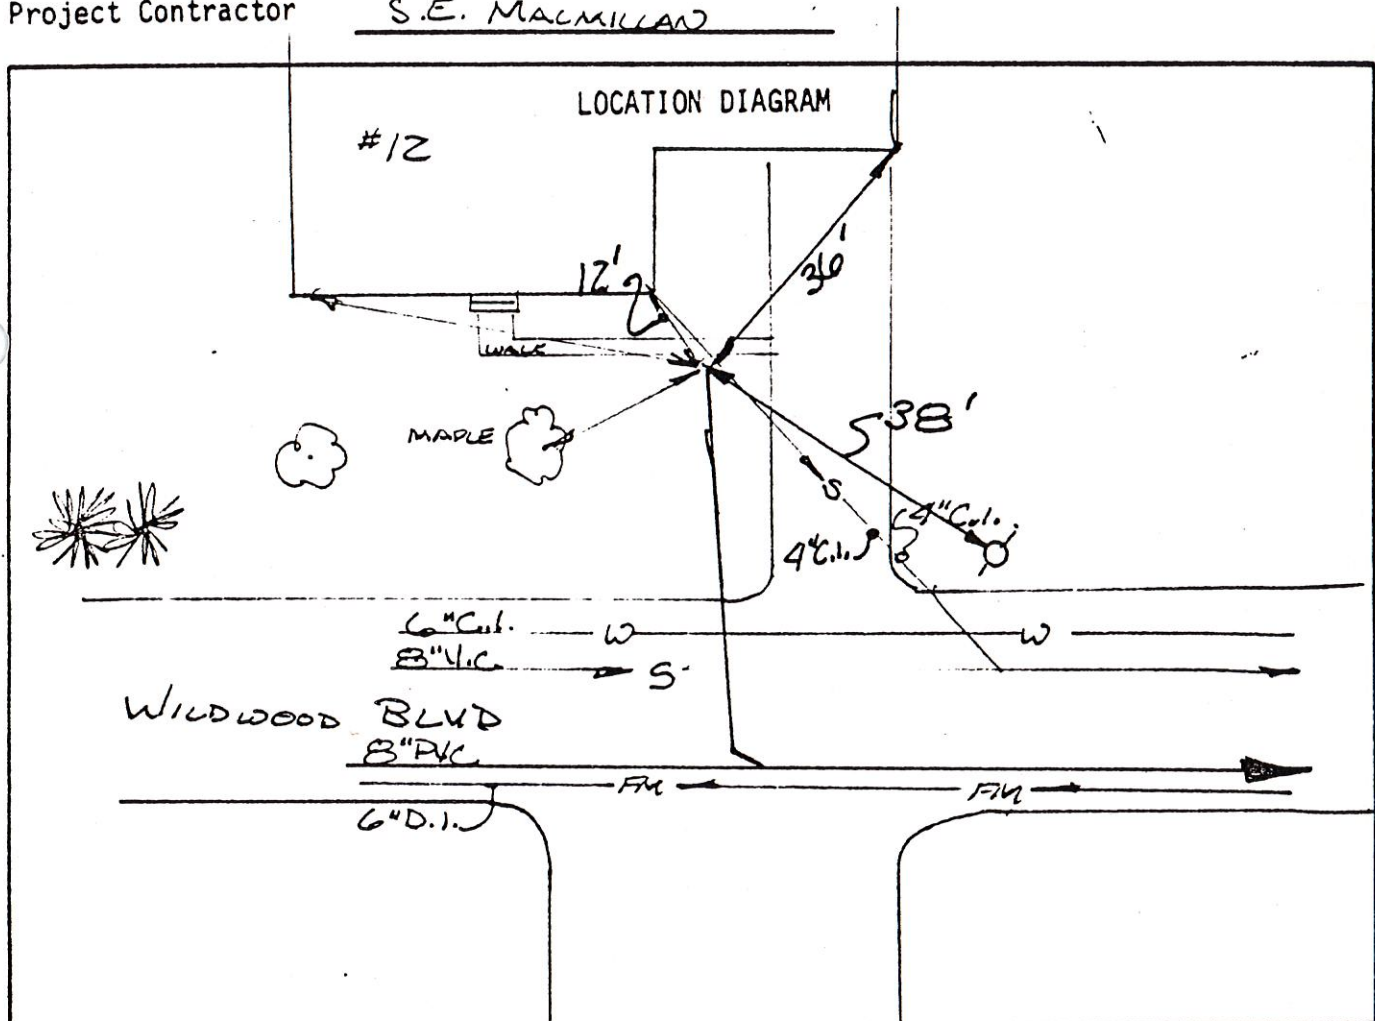

Remarks: 6" PVC GOES UNDER 8" V.C. BY 1' + & UNDER 6" C.I. BY 1'
NEED 6" X 9" REDUCER & 45° BEND TO CONNECT.

SAMPLE BUILDING SEWER SKETCH

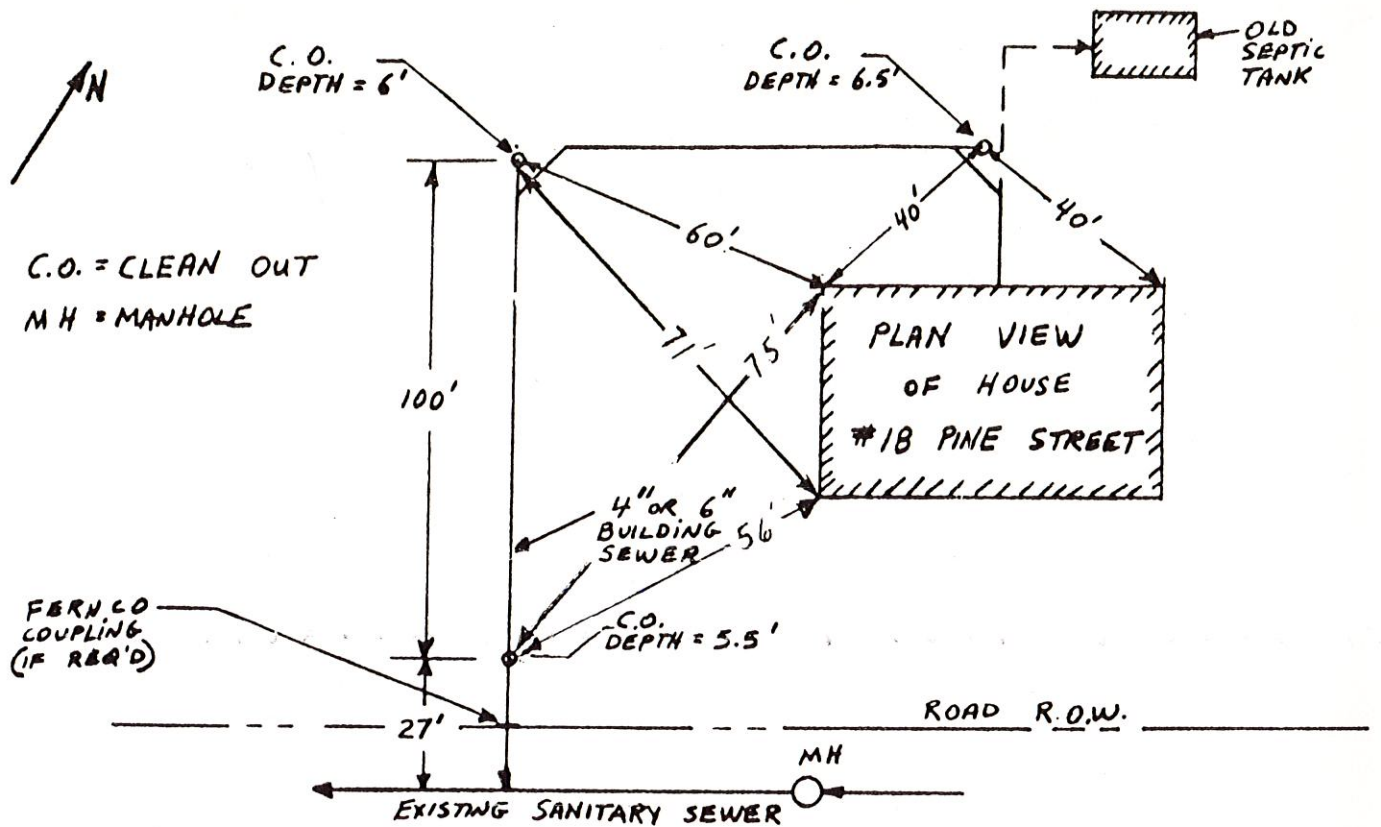


NAME: Kerry Jackson

ADDRESS: 12 Wildwood

CONTRACTOR: Scott Dyer

DATE: 7-9-84

COLLECTOR OR INTERCEPT

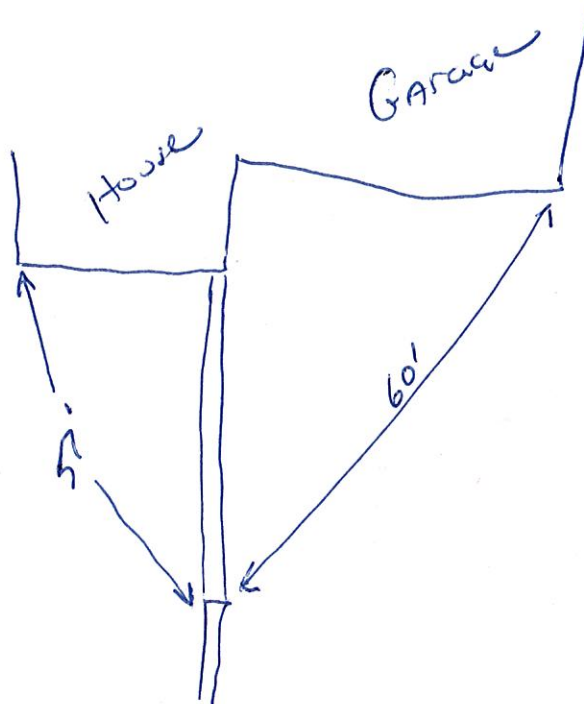

4' deep

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed JUNE 28, 1983

Street WILDWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 15

Connection at Sewer Main WYE

Occupant _____


Depth, End of Service Pipe 5 1/2'

Owner _____

Length of Service Pipe Laid 19'


Measured, Located By _____

Project Contractor S.E. MACMILLAN

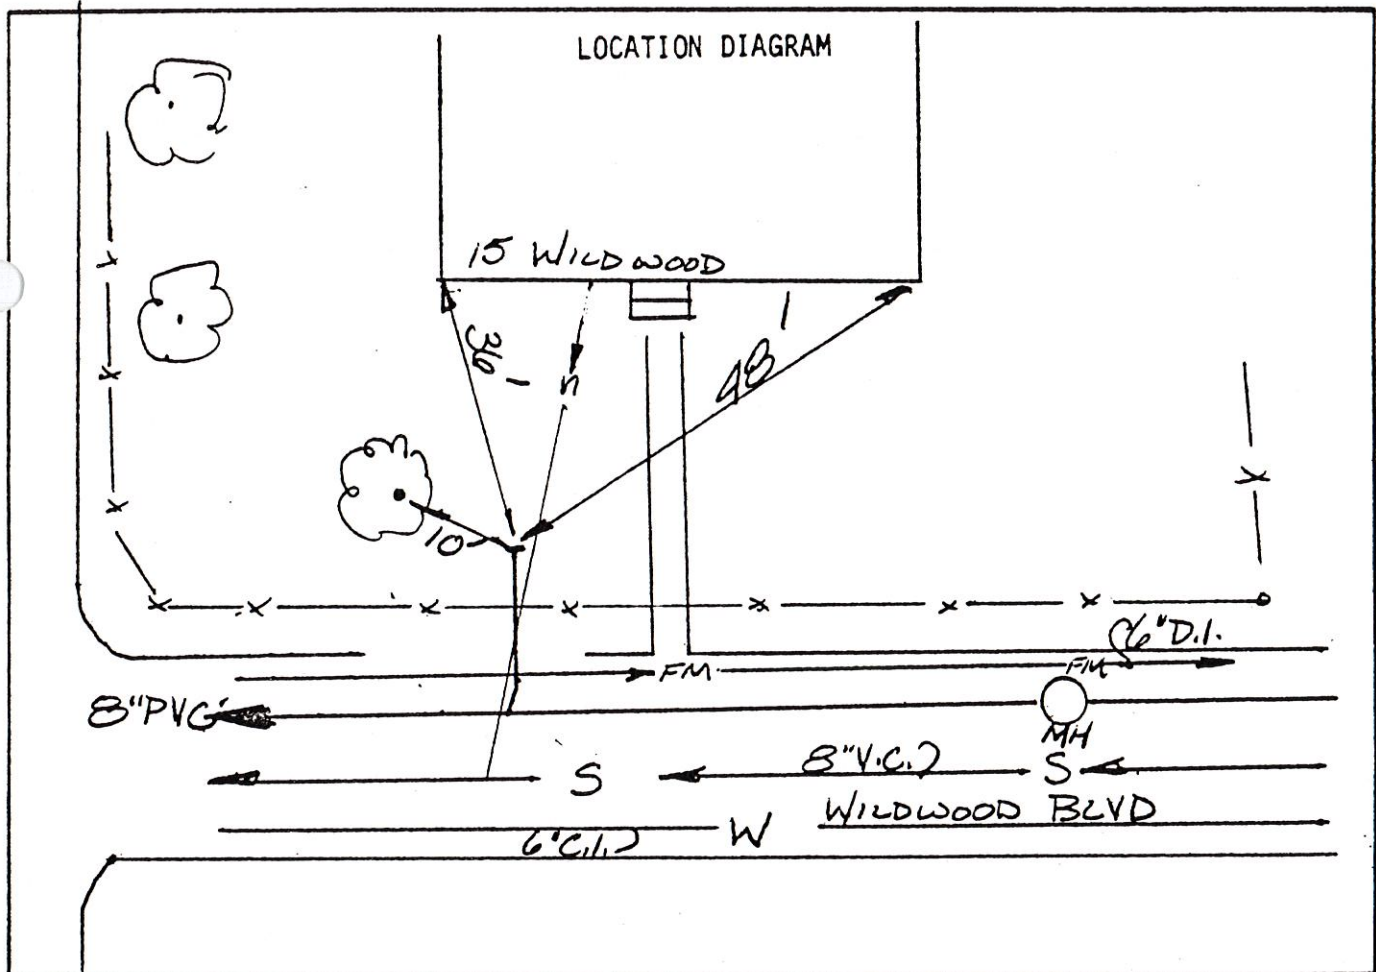

Remarks: 6" PVC C.P. & RIGHT UNDER EXISTING 9" CAST IRON SEWER

SAMPLE BUILDING SEWER SKETCH

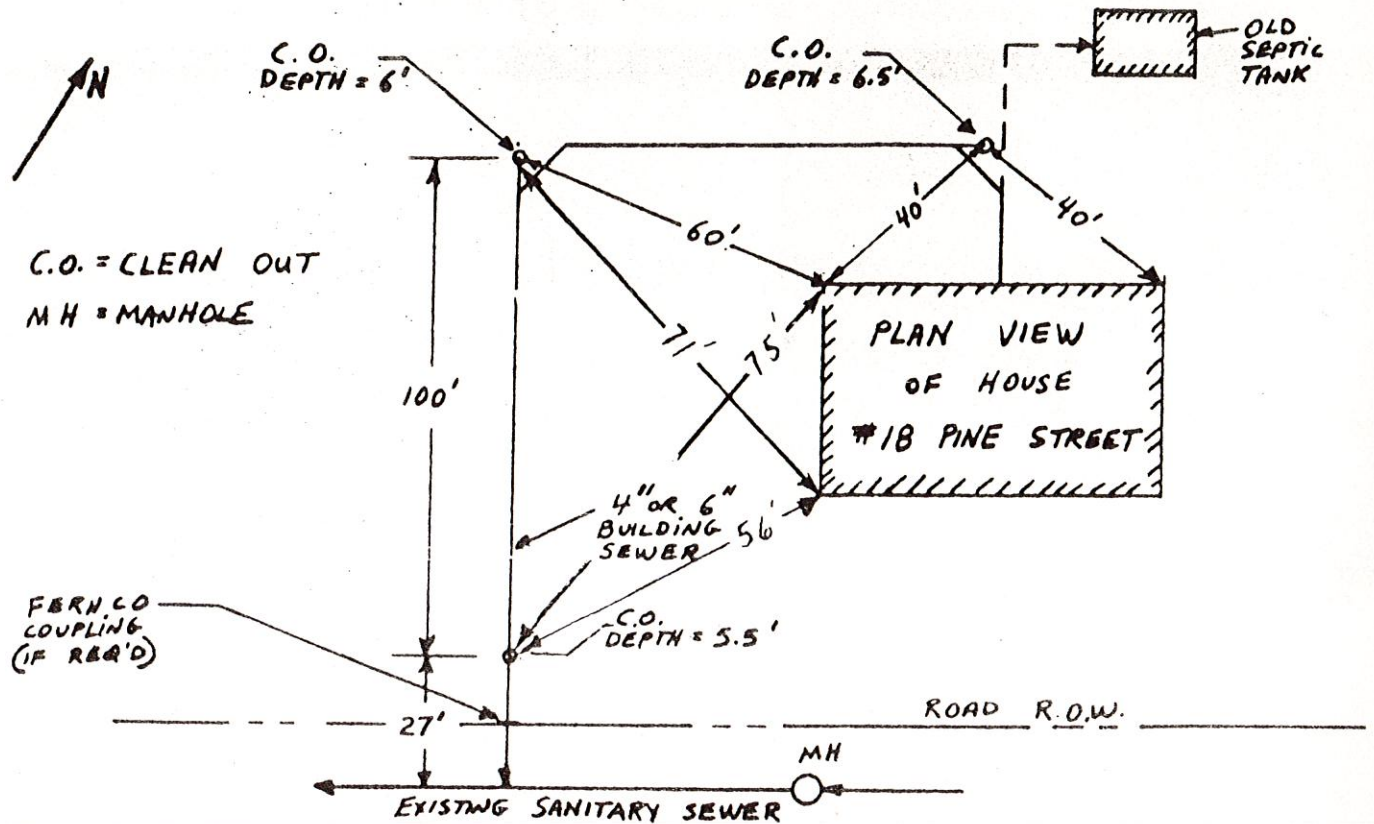


NAME: Ed Stern

ADDRESS: 15 Wildwood

CONTRACTOR: Scott Dugas

DATE: 6-15-84

COLLECTOR OR INTERCEPT

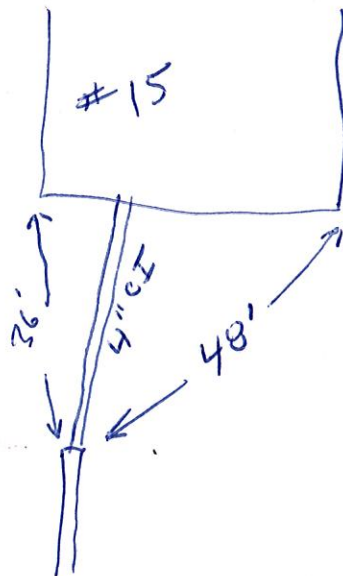

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed JUNE 27, 1983

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 16

Connection at Sewer Main WYE

Occupant _____


Depth, End of Service Pipe 6'

Owner _____

Length of Service Pipe Laid 36'

Measured, Located By _____

Project Contractor S.E. MACMILLAN

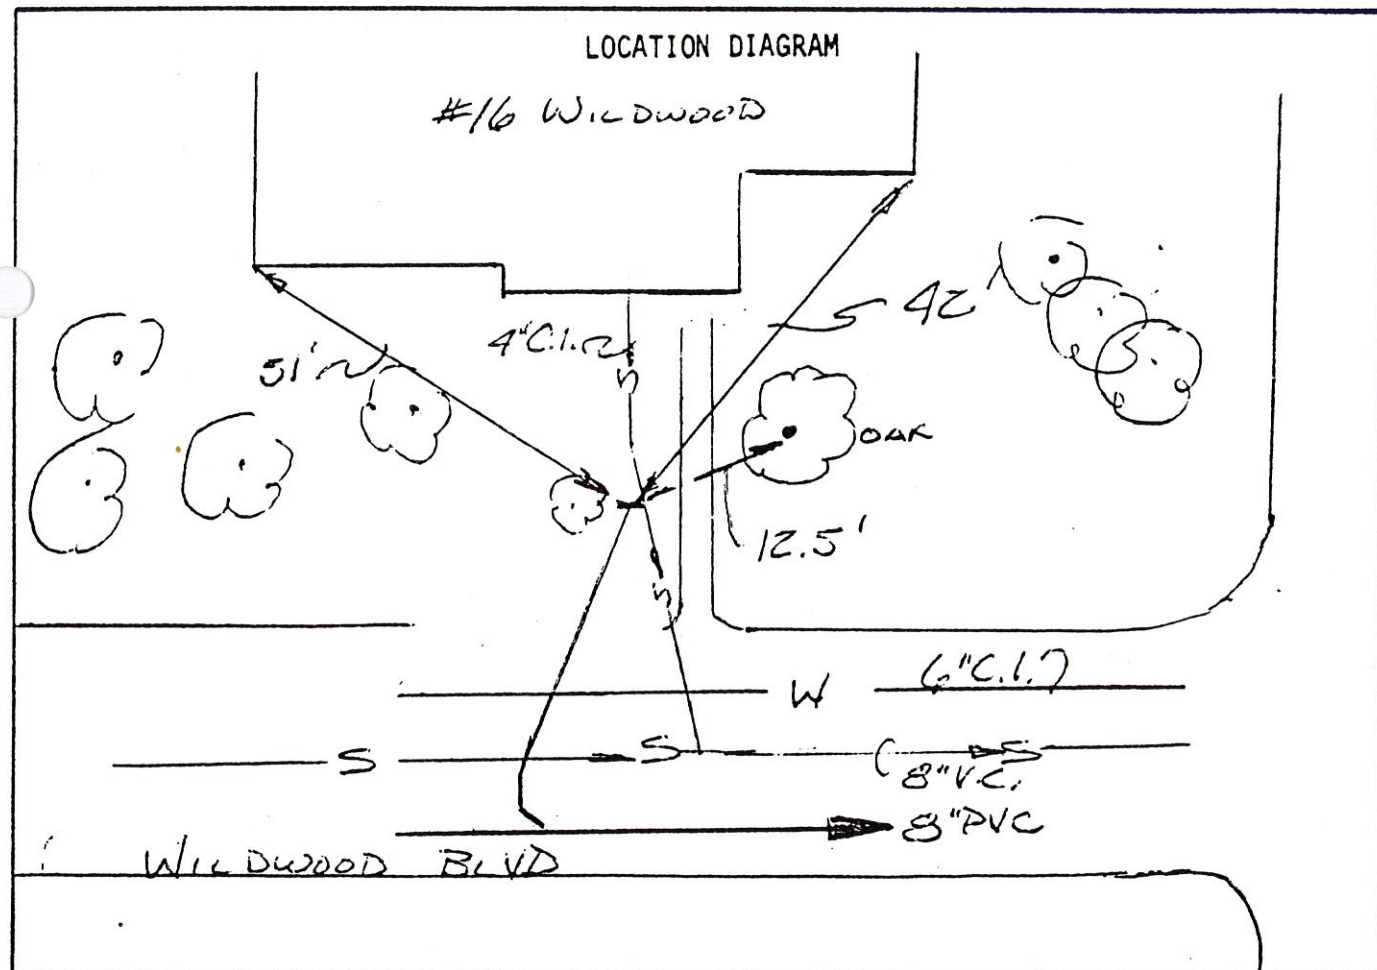

Remarks: 6" PVC GOES UNDER EXISTING 8" SEWER & WATER MAIN. CONNECTION TO BE MADE LATER

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed July 16, 1983

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 19

Connection at Sewer Main WYE

Occupant _____


Depth, End of Service Pipe 4'

Owner _____

Length of Service Pipe Laid 39.5'

Measured, Located By _____

Project Contractor S E. MACMILLAN

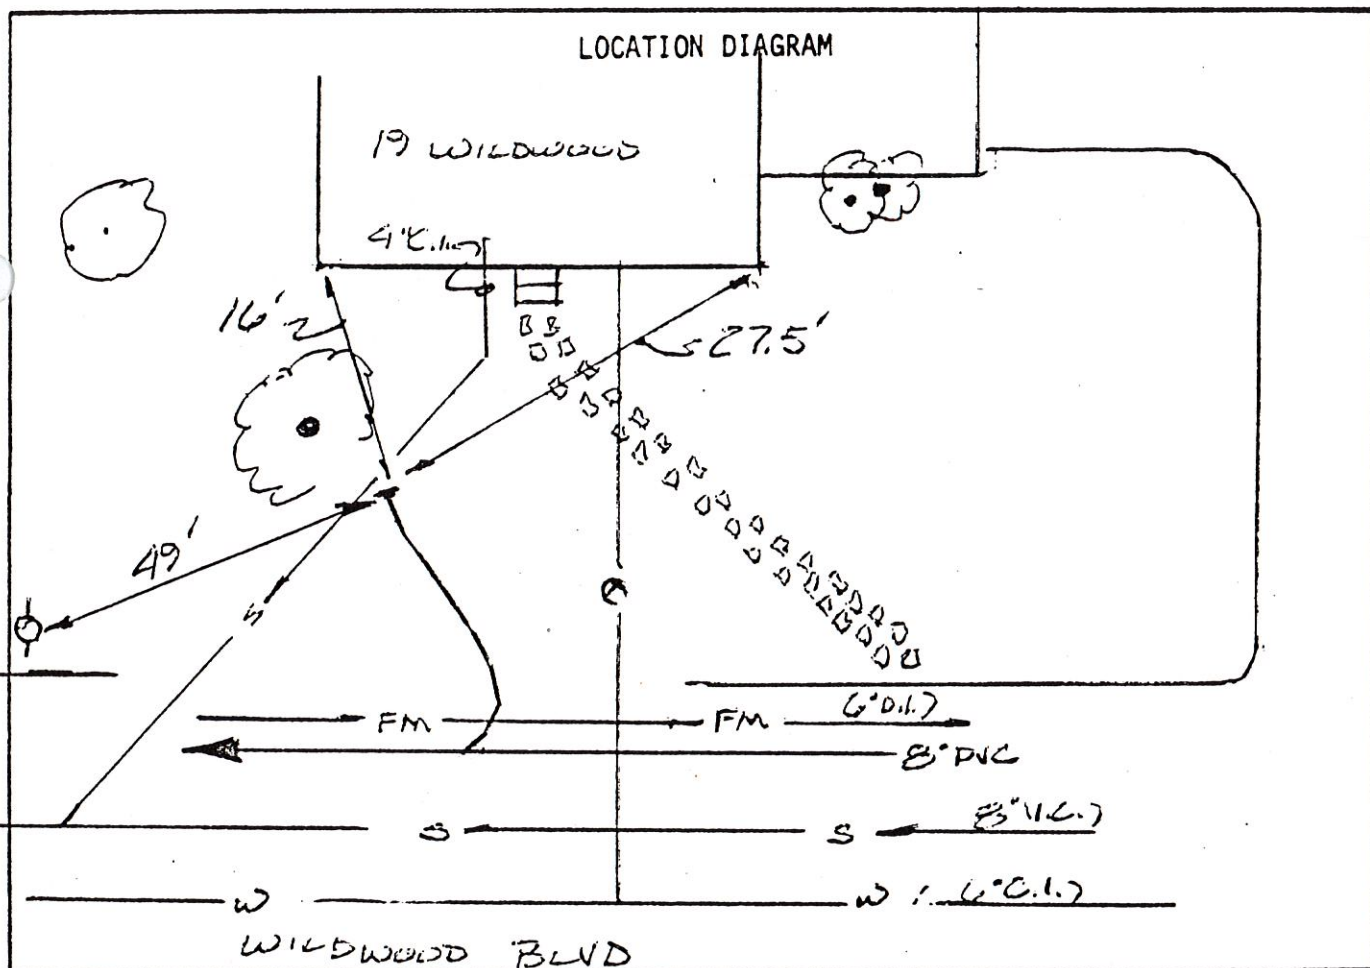

Remarks: NEED 45° BEND & 6" X 4" REDUCER TO CONNECT TO
EXISTING 9" CAST IRON SEWER.

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed JULY 6, 1983

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 20

Connection at Sewer Main WYE

Occupant _____


Depth, End of Service Pipe 7'

Owner _____

Length of Service Pipe Laid 28.5'

Measured, Located By _____

Project Contractor S.E. MCMILLAN

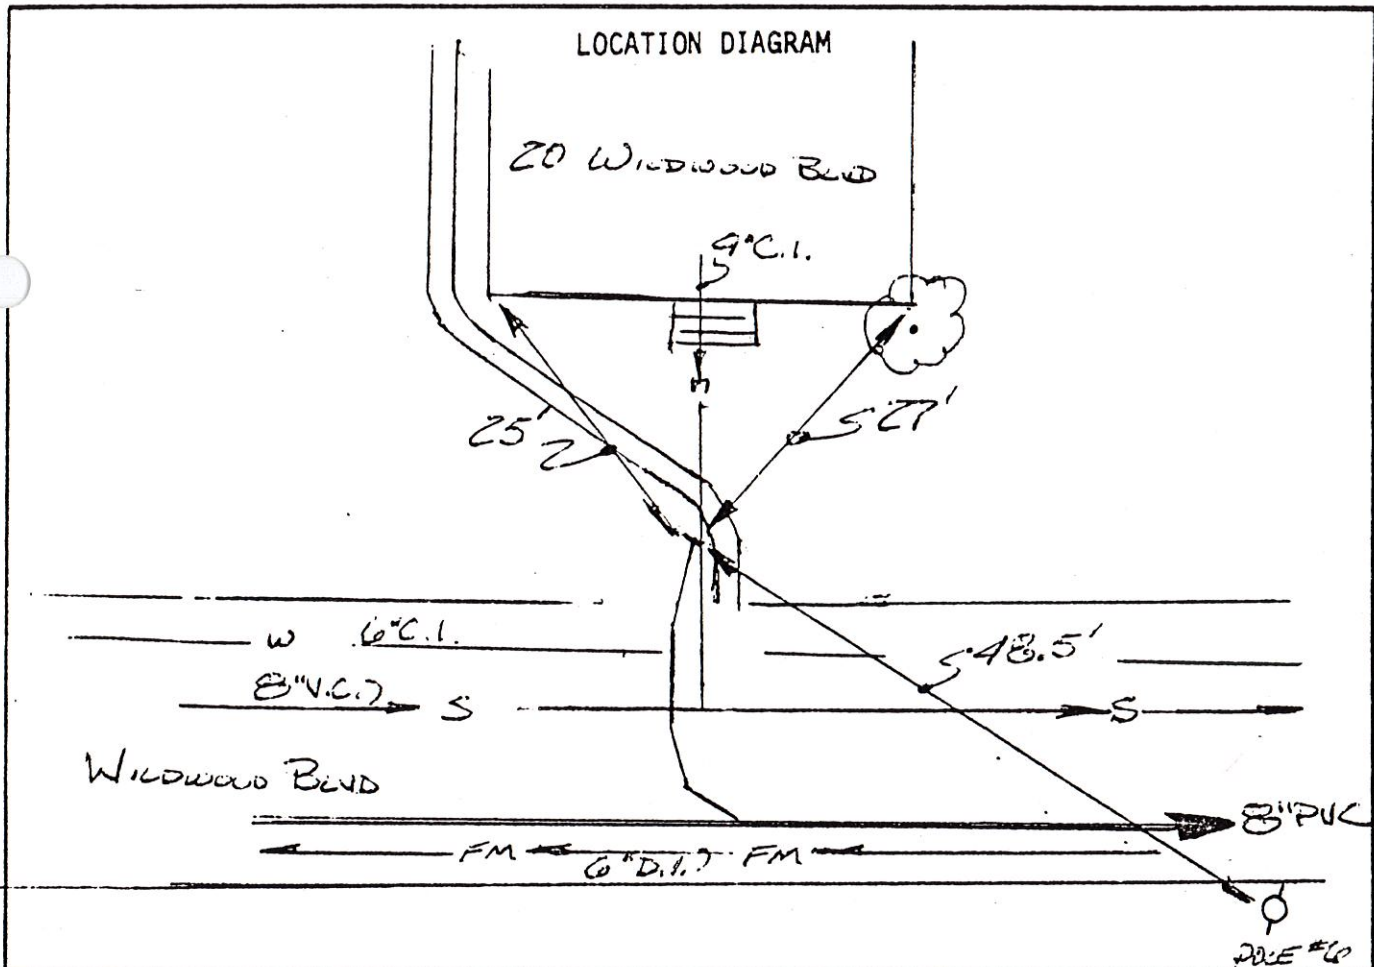

Remarks: 6" PVC GOES UNDER 8" V.C. & 6" C.I. - NEED 220 BEND &
6" & 4" REDUCER TO CONNECT TO EXISTING 4" CAST IRON SEWER.

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/26/83

Street WILDWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 21

Connection at Sewer Main 8" x 6" CAST IRON SADDLE

Occupant _____

Depth, End of Service Pipe 4' @ EXISTING SEWER


Owner _____

Length of Service Pipe Laid 12'

Measured, Located By _____

Project Contractor S. E. MACMILLAN

2 TEST PITS - PAY ITEM
LOCATE EXISTING SEWER
7/7/83

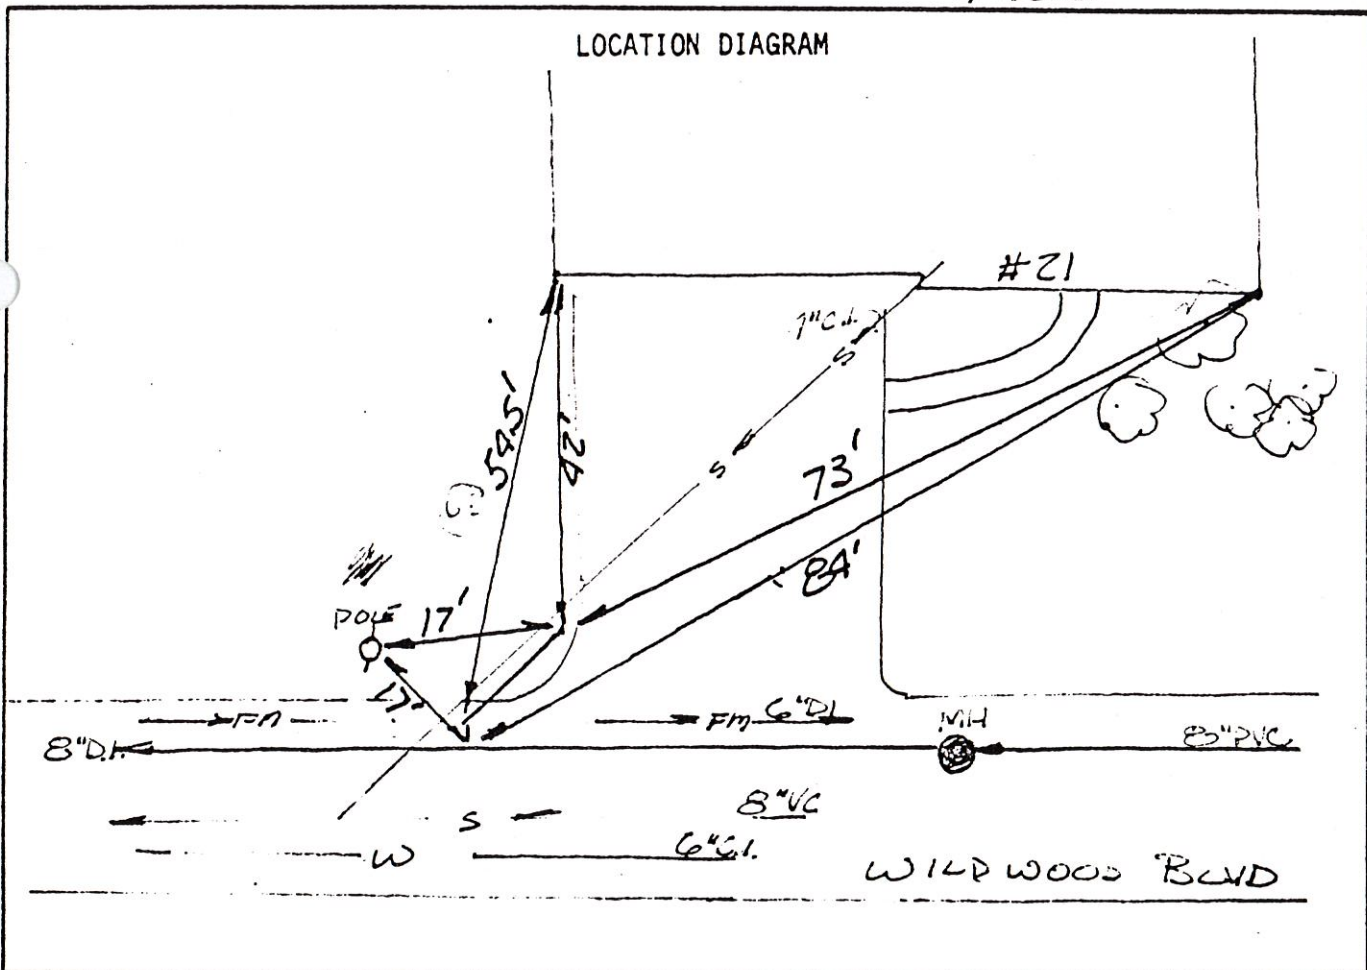

Remarks: NEED 6" x 9" REDUCER to connect

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed JULY 23, 1983

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 22

Connection at Sewer Main EAST IRON SADDLE

Occupant _____

Depth, End of Service Pipe 3.5'


Owner _____

Length of Service Pipe Laid 35.5'

Measured, Located By _____

Project Contractor S.E. MAHALLAN

LOCATION DIAGRAM

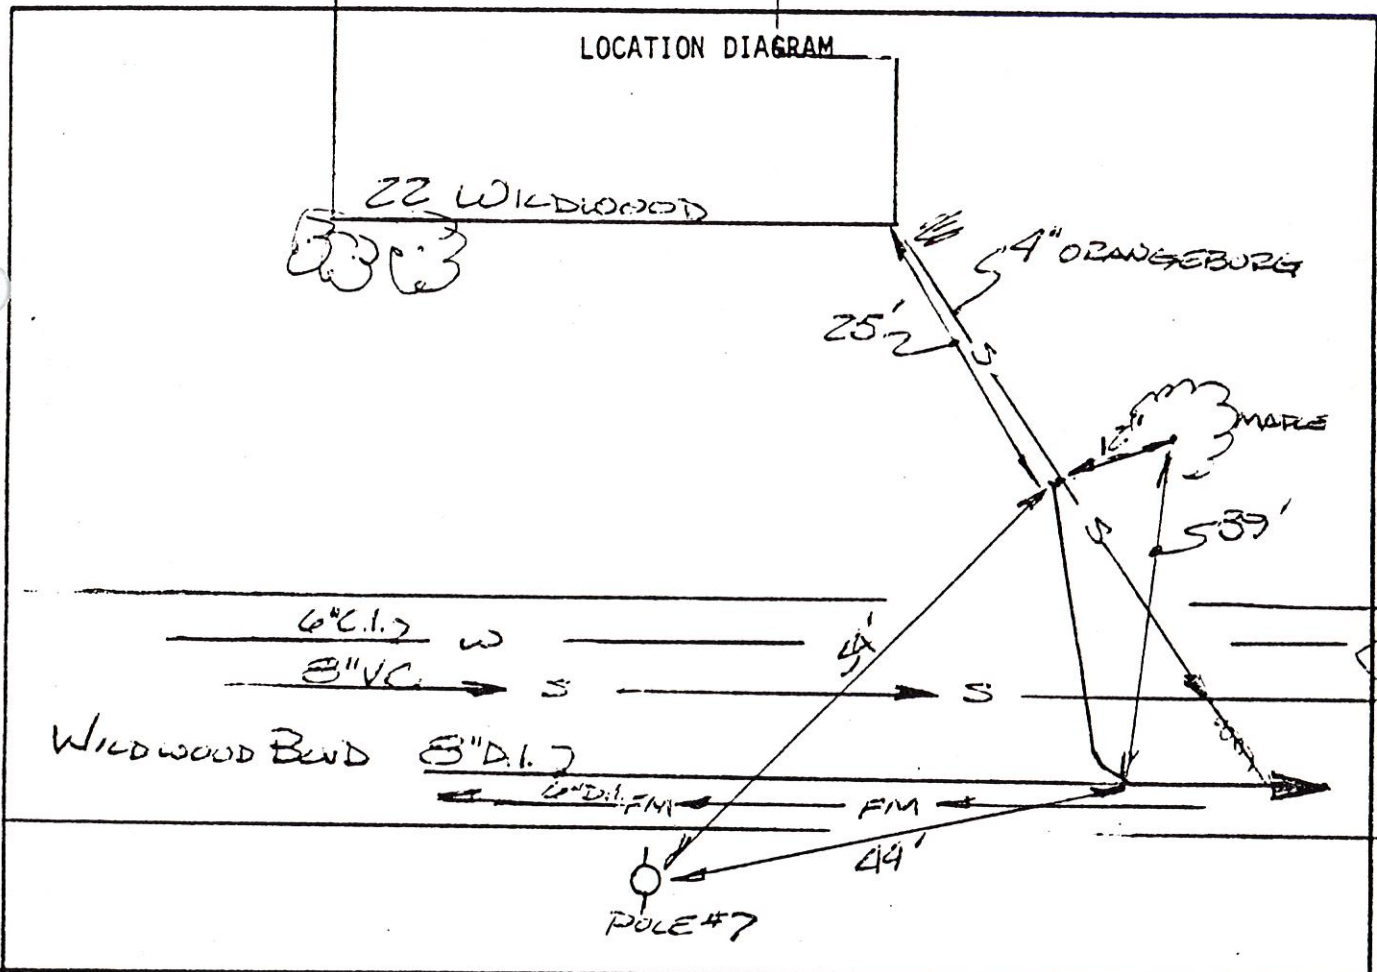

Remarks: 6" PVC GOES UNDER 8" VC & OVER 6" C.I.
NEED 22° BEND & 6" X 4" REDUCER TO CONNECT TO EXISTING
4" ORANGEBOURG SEWER.

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/26/83

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 23

Connection at Sewer Main 8" X 6" CAST IRON SADDLE

Occupant _____


Depth, End of Service Pipe 3.5' @ EXISTING SEWER

Owner _____

Length of Service Pipe Laid 18.5' OF 6" PVC


Measured, Located By _____

Project Contractor S.E. MACMILLAN

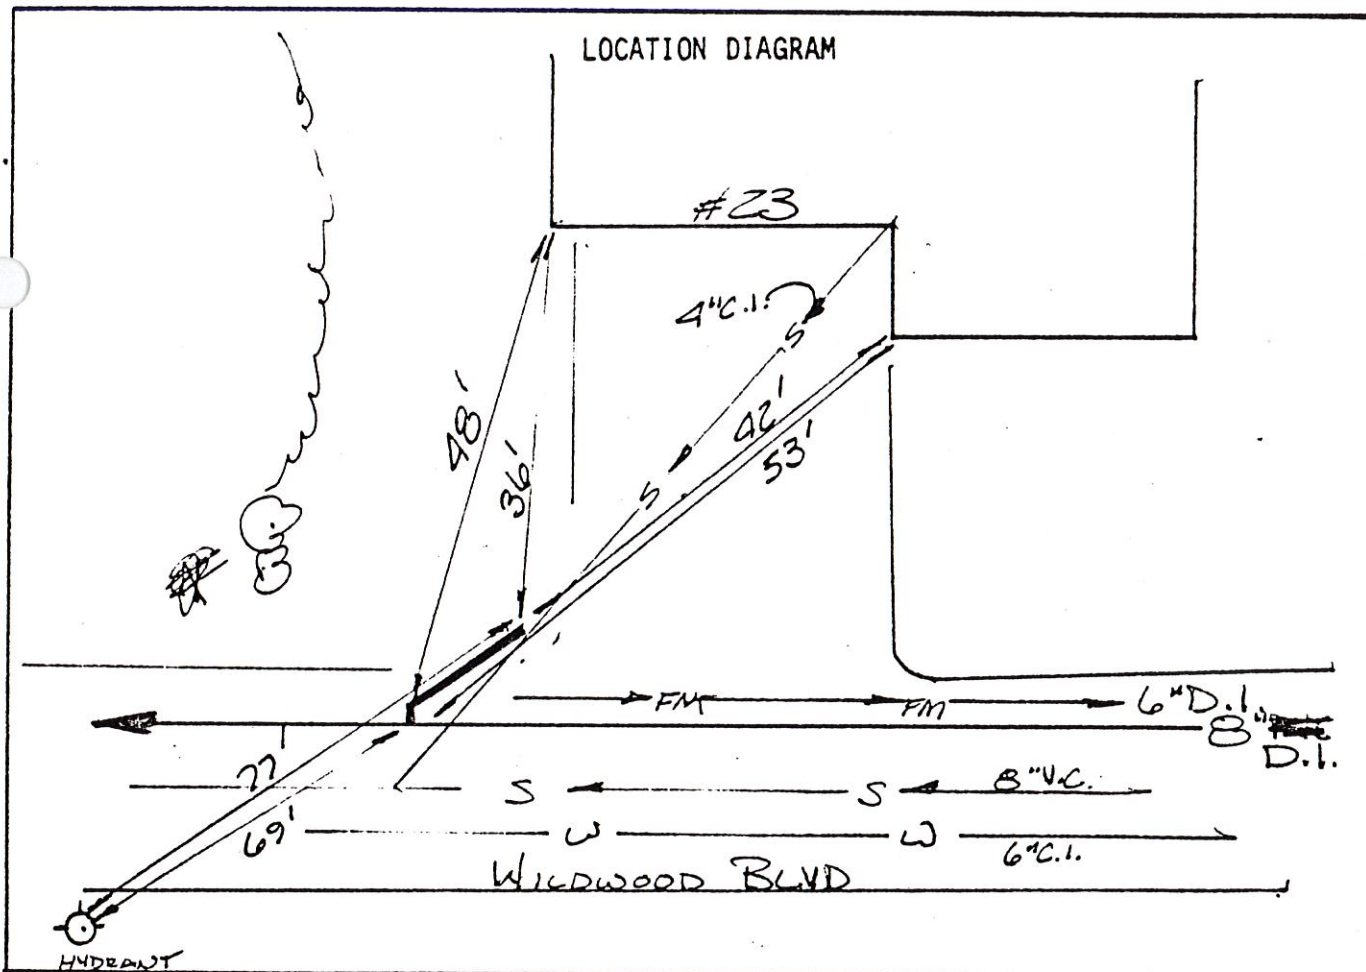


Remarks: LAID 6" PVC TO EDGE OF PAVED DRIVEWAY & SHORT OF IT TO
AVOID TRENCHING INTO DRIVEWAY. CONNECTION TO EXISTING TO BE
MADE @ EDGE OF DRIVEWAY WITH 6" X 4" REDUCER.

SAMPLE BUILDING SEWER SKETCH

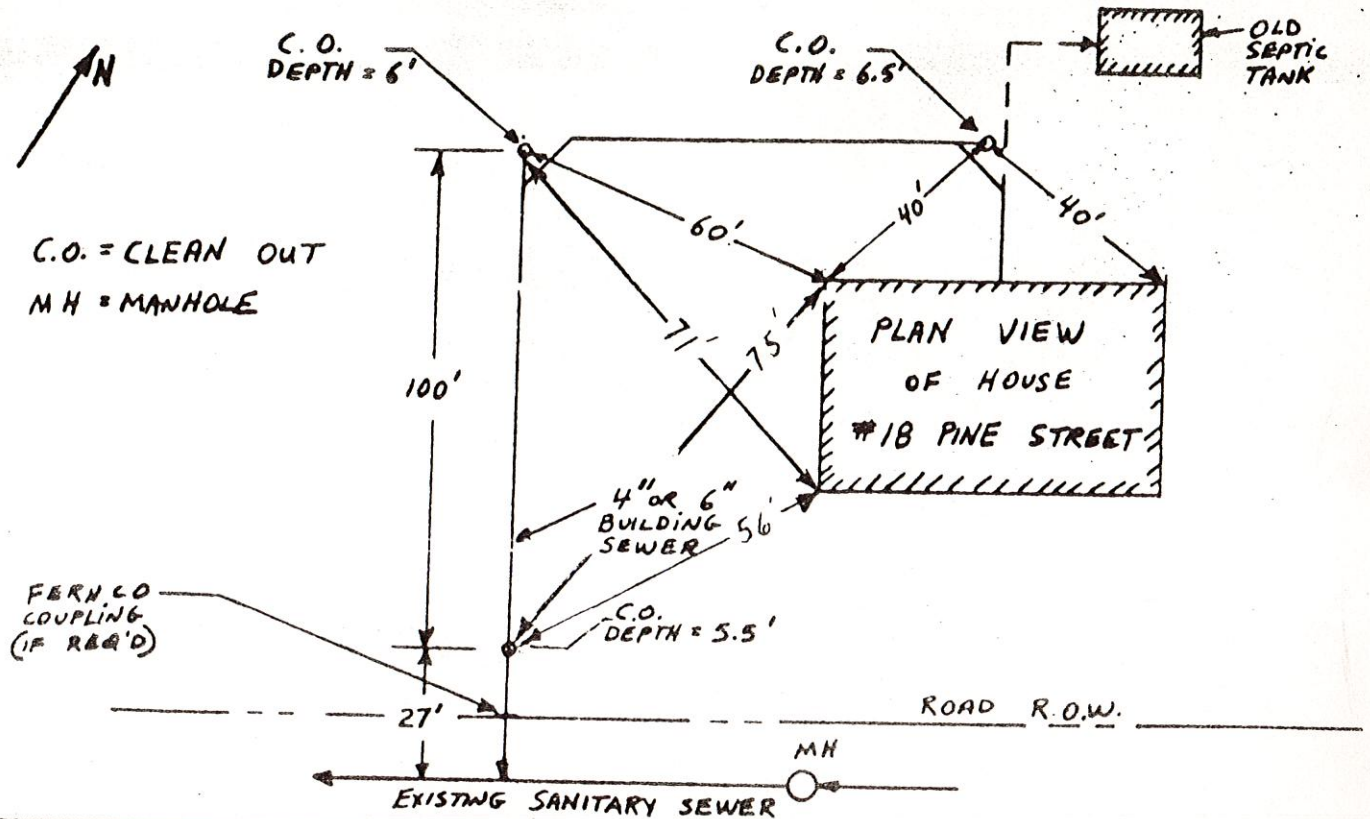

NAME: McDonald
 ADDRESS: 23 Wildwood
 CONTRACTOR: Scott Nuyes

DATE: 6-15-94
 COLLECTOR OR INTERCEPTOR

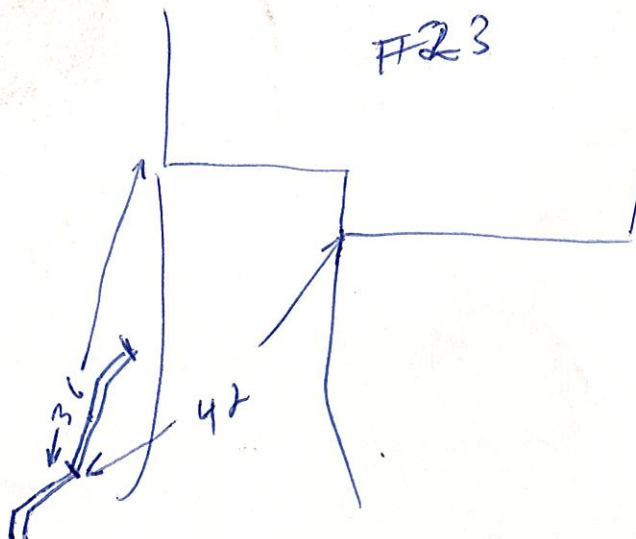

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/27/83

Street WILDWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 25

Connection at Sewer Main 8" x 6" CAST IRON SADDLE

Occupant _____

Depth, End of Service Pipe 3.5' @ EXISTING SEWER


Owner _____

Length of Service Pipe Laid 27'

Measured, Located By _____


Project Contractor S.E. MACMILLAN

LOCATION DIAGRAM

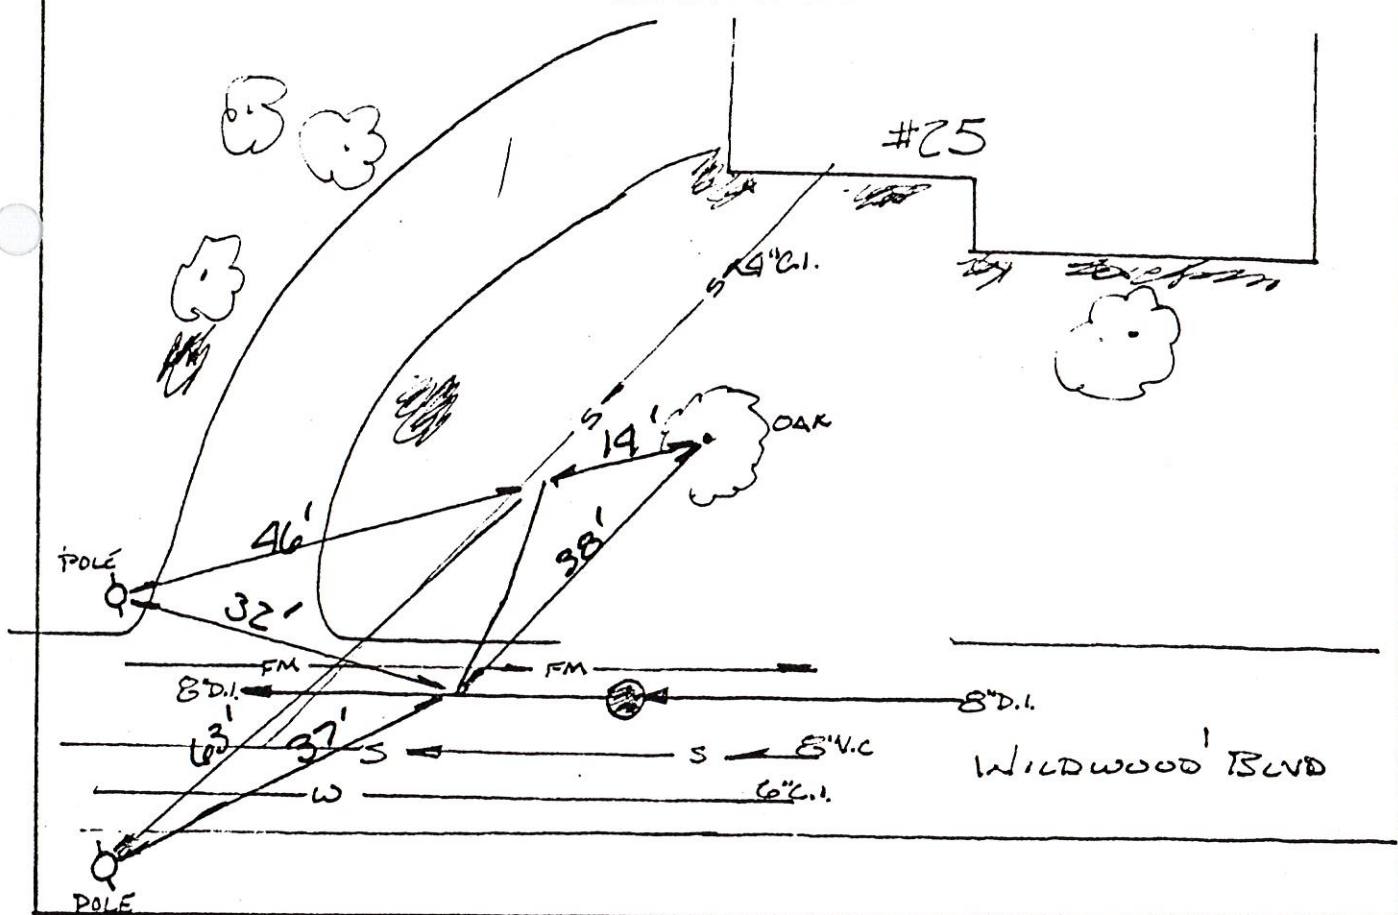


Remarks: NEED 22° BEND & 6\" x 9\" REDUCER TO CONNECT.

SAMPLE BUILDING SEWER SKETCH

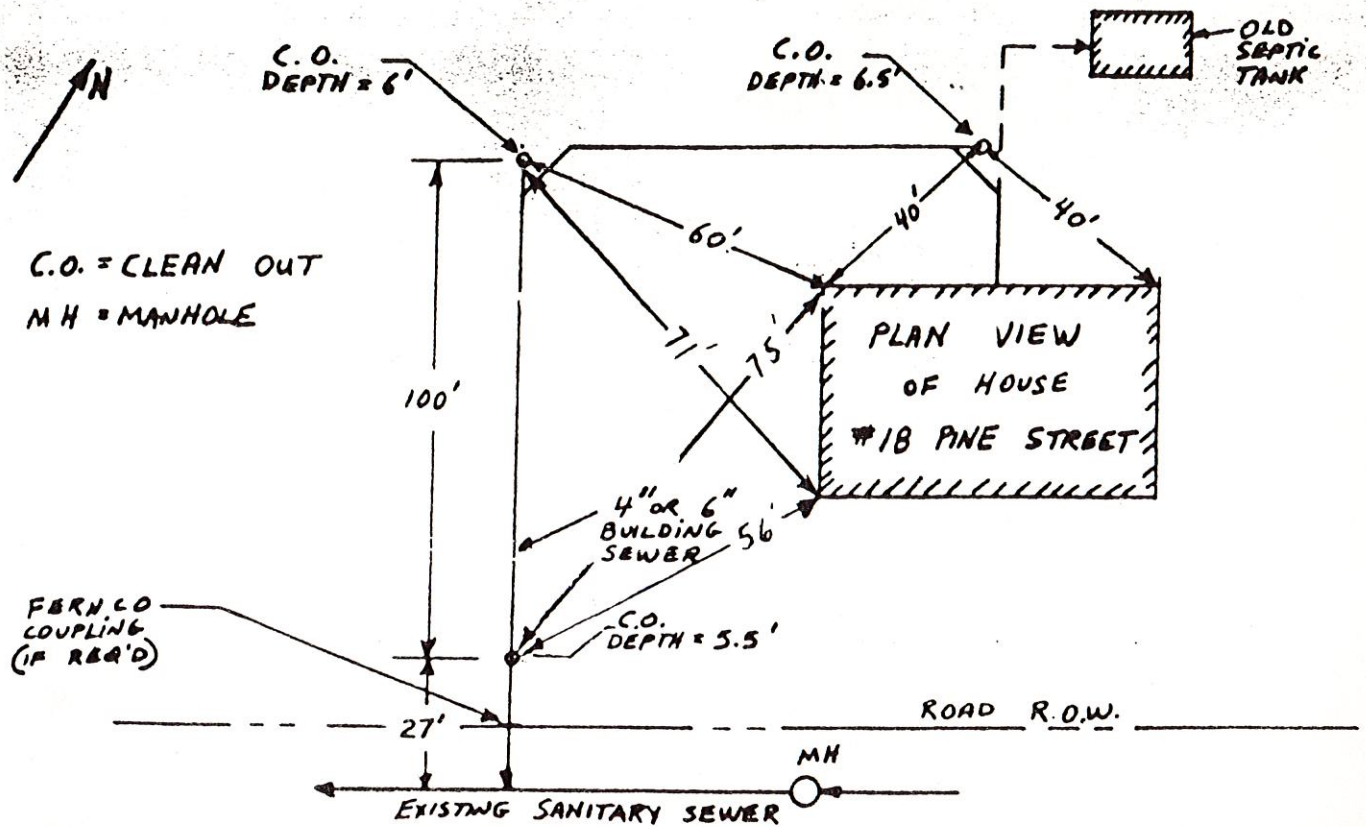

NAME: Sylvia Bannan
 ADDRESS: 25 Wildwood Bldg.
 CONTRACTOR: Scott Dyer

DATE: 6-15-84
 COLLECTOR OR INTERCEPT

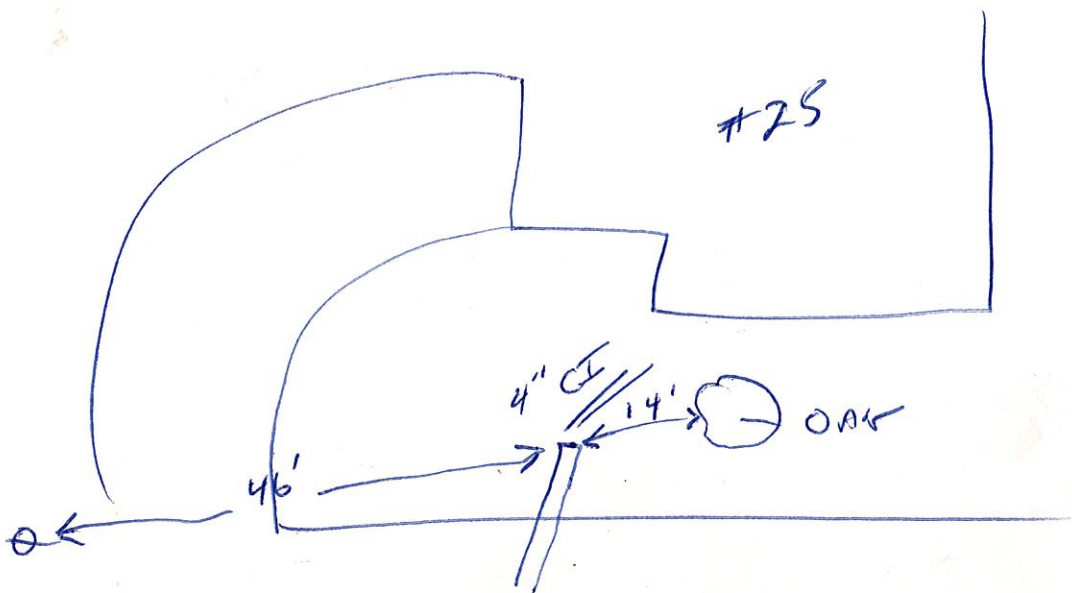

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/27/83

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 26

Connection at Sewer Main 8" x 16" CAST IRON SADDLE

Occupant _____


Depth, End of Service Pipe 3.5' EXISTING SEWER

Owner _____

Length of Service Pipe Laid 38'

Measured, Located By _____

Project Contractor S.E. MACMILLAN

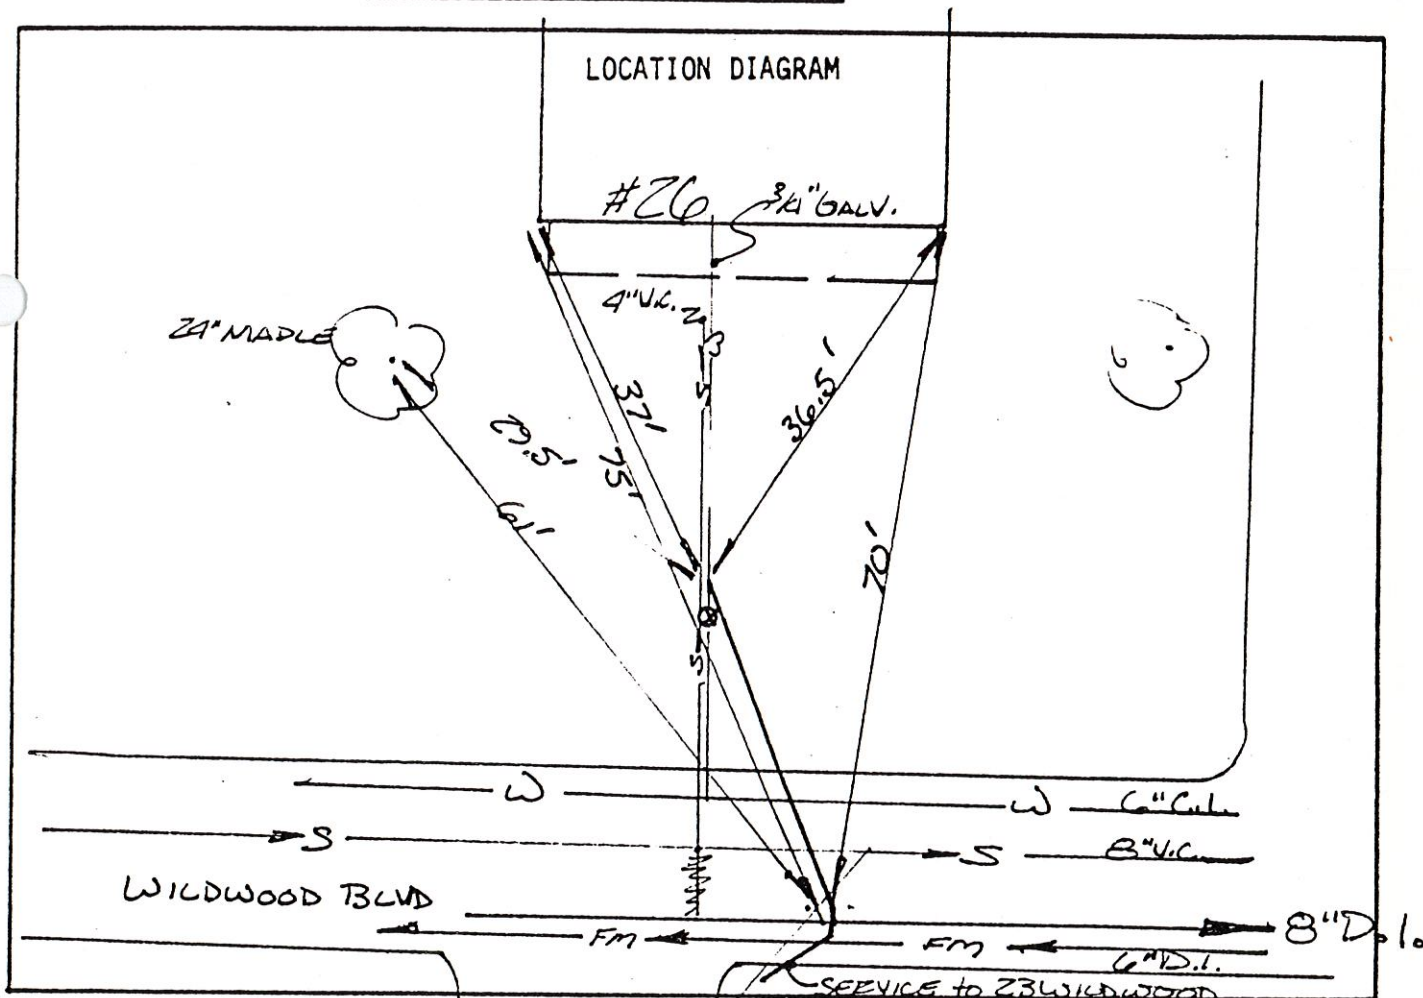

Remarks: 6" PVC GOES UNDER 8" V.C. SEWER & 6" WATER MAIN.
NEED 6" x 4" REDUCER & 22° BEND TO CONNECT 3/4" GALVANIZED
WATER JUST ABOVE 4" V.C. SEWER.

4" C.I. SEWER to 23 WILLOWOOD

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/27/83

Street WILDWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 29

Connection at Sewer Main 8" x 6" CAST IRON SADDLE

Occupant _____


Depth, End of Service Pipe 6.5'

Owner _____

Length of Service Pipe Laid 25.5'


Measured, Located By _____

Project Contractor S.E. MACMILLAN

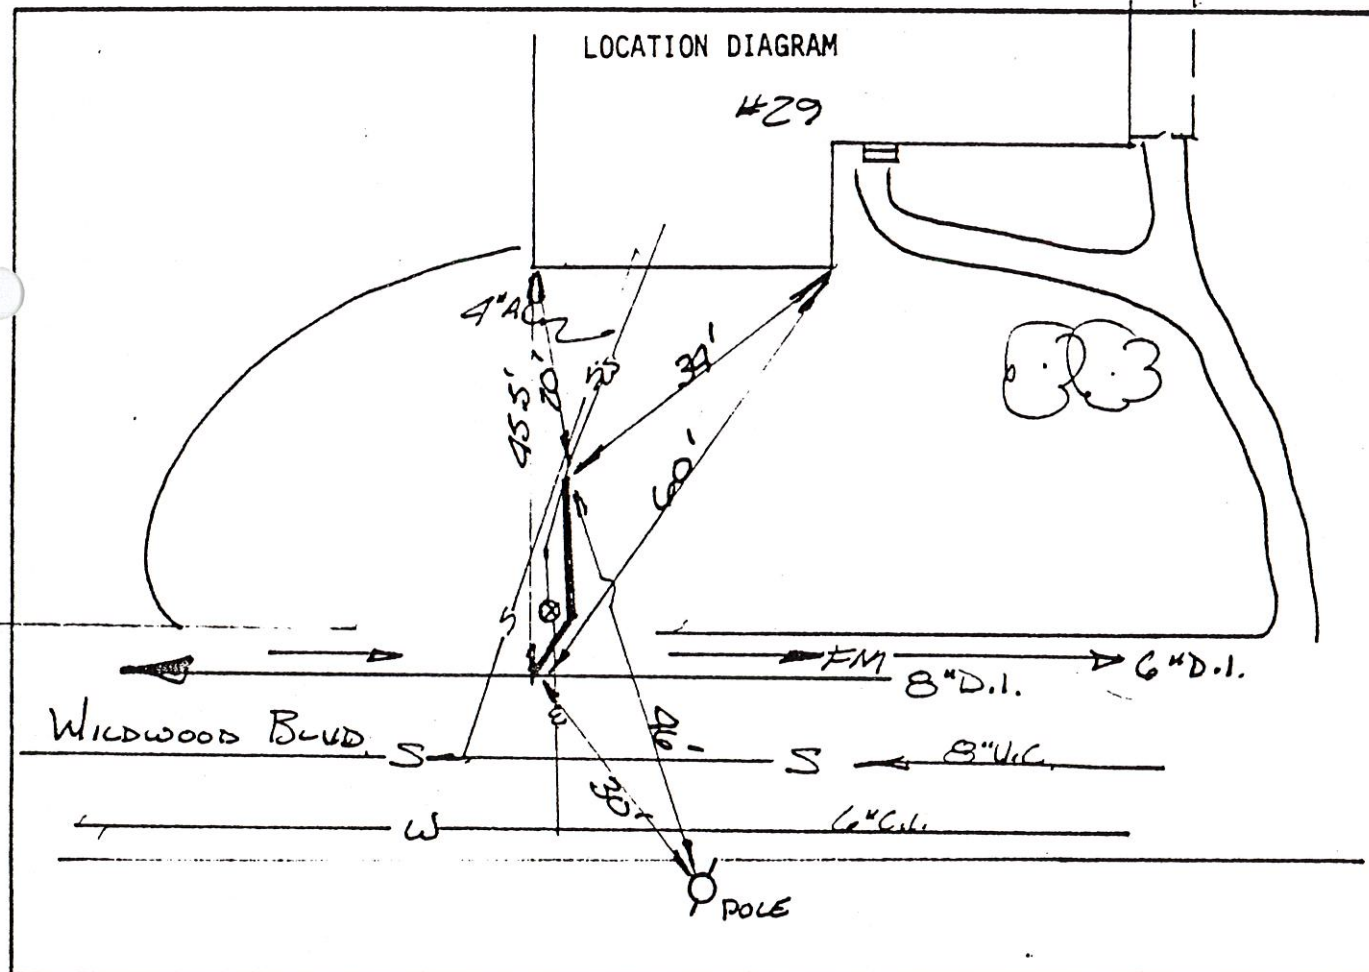


Remarks: NEED 6" x 8" REDUCER TO CONNECT

SAMPLE BUILDING SEWER SKETCH

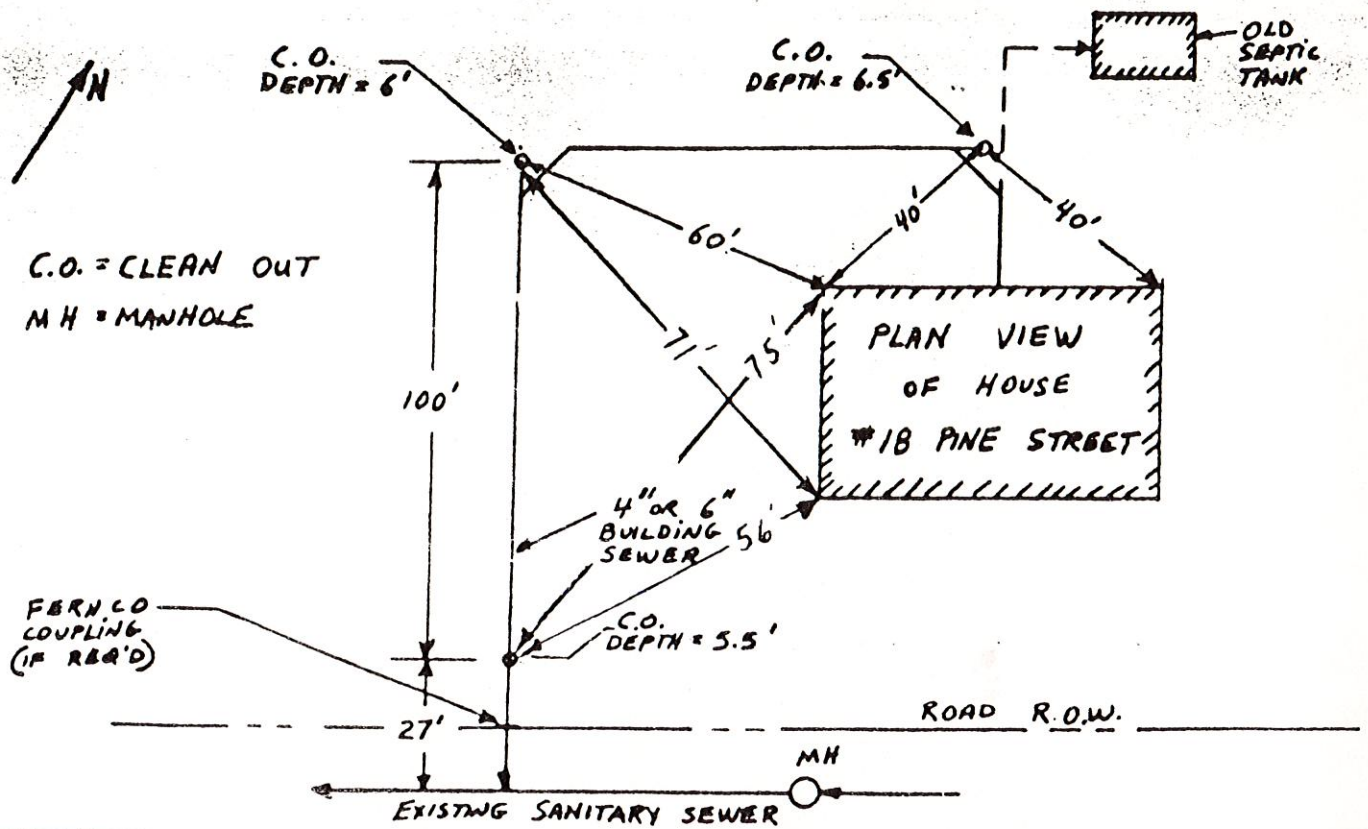

NAME: George Bradford
 ADDRESS: 29 Wildwood
 CONTRACTOR: Scott Ouyas

DATE: 6-15-84
 COLLECTOR OR INTERCEPTOR

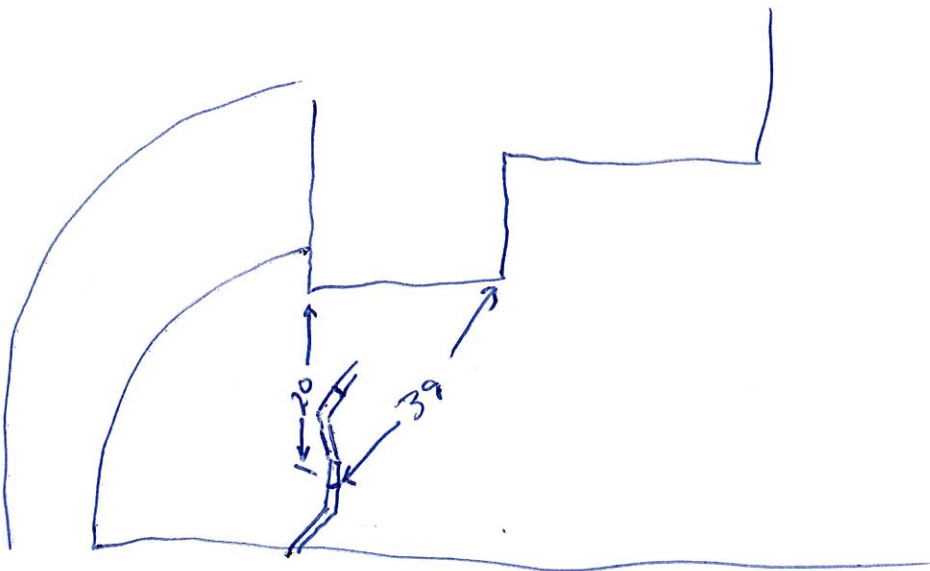

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/28/83

Street WILDWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 30

Connection at Sewer Main 8" X 6" CAST IRON SADDLE

Occupant _____


Depth, End of Service Pipe 4.5' @ EXISTING SEWER

Owner _____

Length of Service Pipe Laid 38.5'

Measured, Located By _____

Project Contractor S.E. MACMILLAN

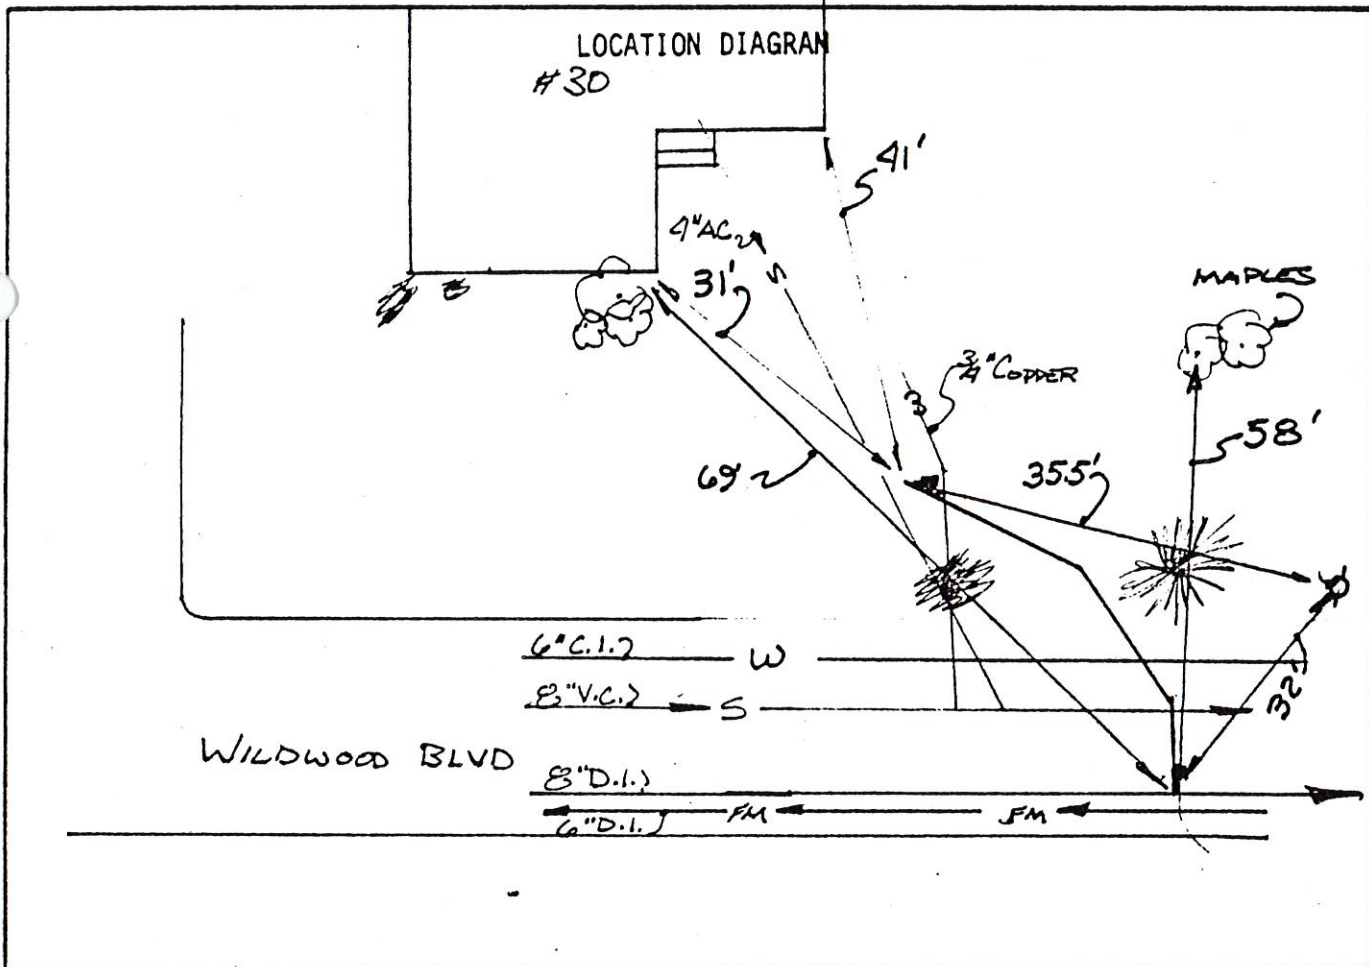


Remarks: 6" PVC GOES UNDER 8" V.C. BY 3' & UNDER 6" C.I. BY 1.5'

NEED 6" X 4" REDUCER & 45° BEND TO CONNECT.

3/4" WATER SERVICE IS 1' BACK OF END OF 6" PVC & 1" ABOVE 6" PVC

SAMPLE BUILDING SEWER SKETCH

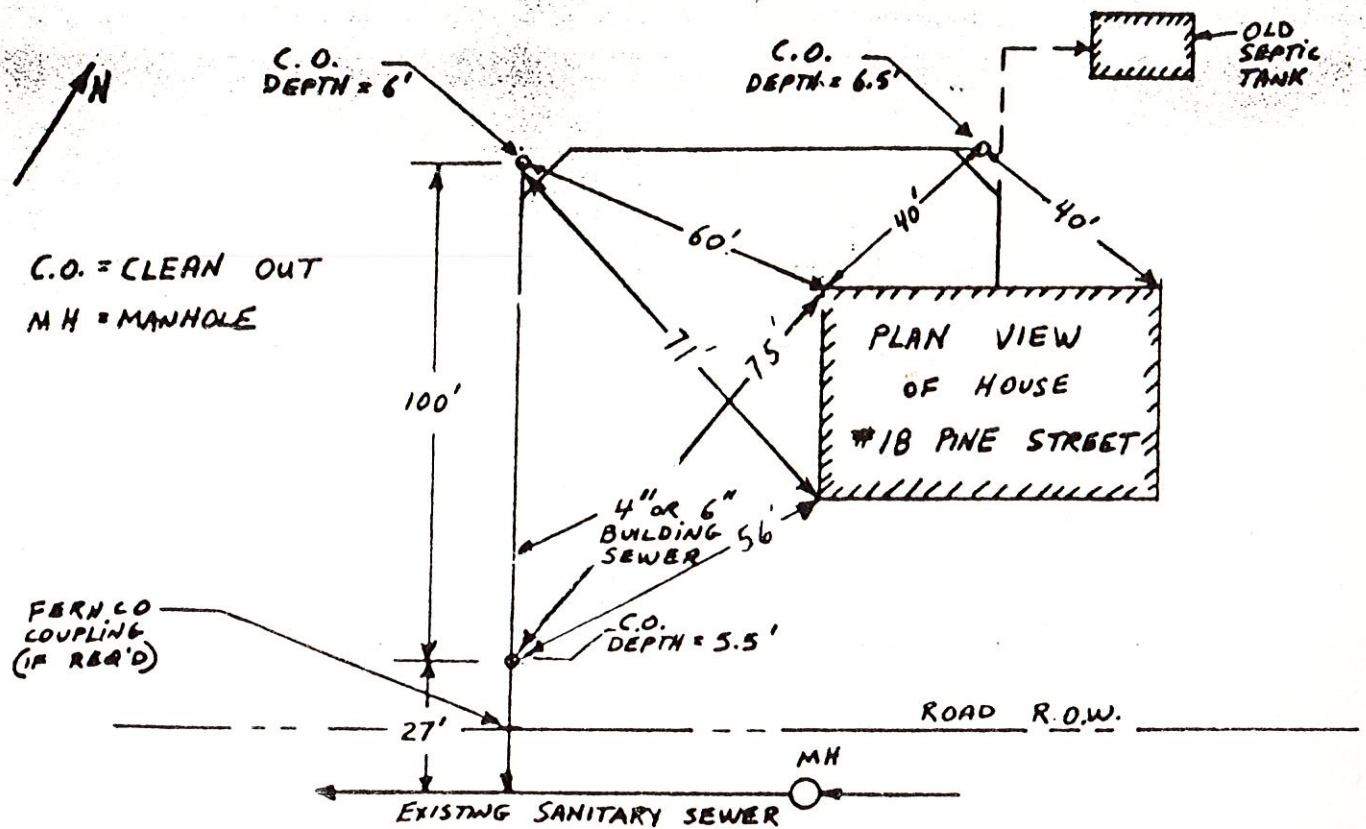


NAME: B York

ADDRESS: 30 Wilwood

CONTRACTOR: Scott Dyer

DATE: 6-15-84

COLLECTOR OR INTERCEPT

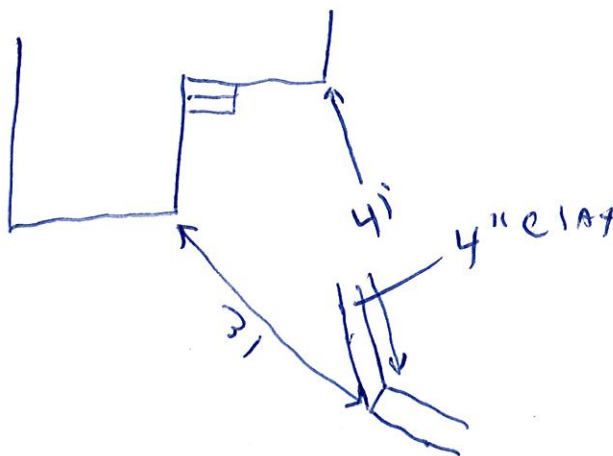

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/29/83

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. # 31

Connection at Sewer Main WVE, MH 41+29'

Occupant _____


Depth, End of Service Pipe 3.5' 2 EXISTING SEWER

Owner _____

Length of Service Pipe Laid 22.5'


Measured, Located By _____

Project Contractor S. E. MACMILLAN

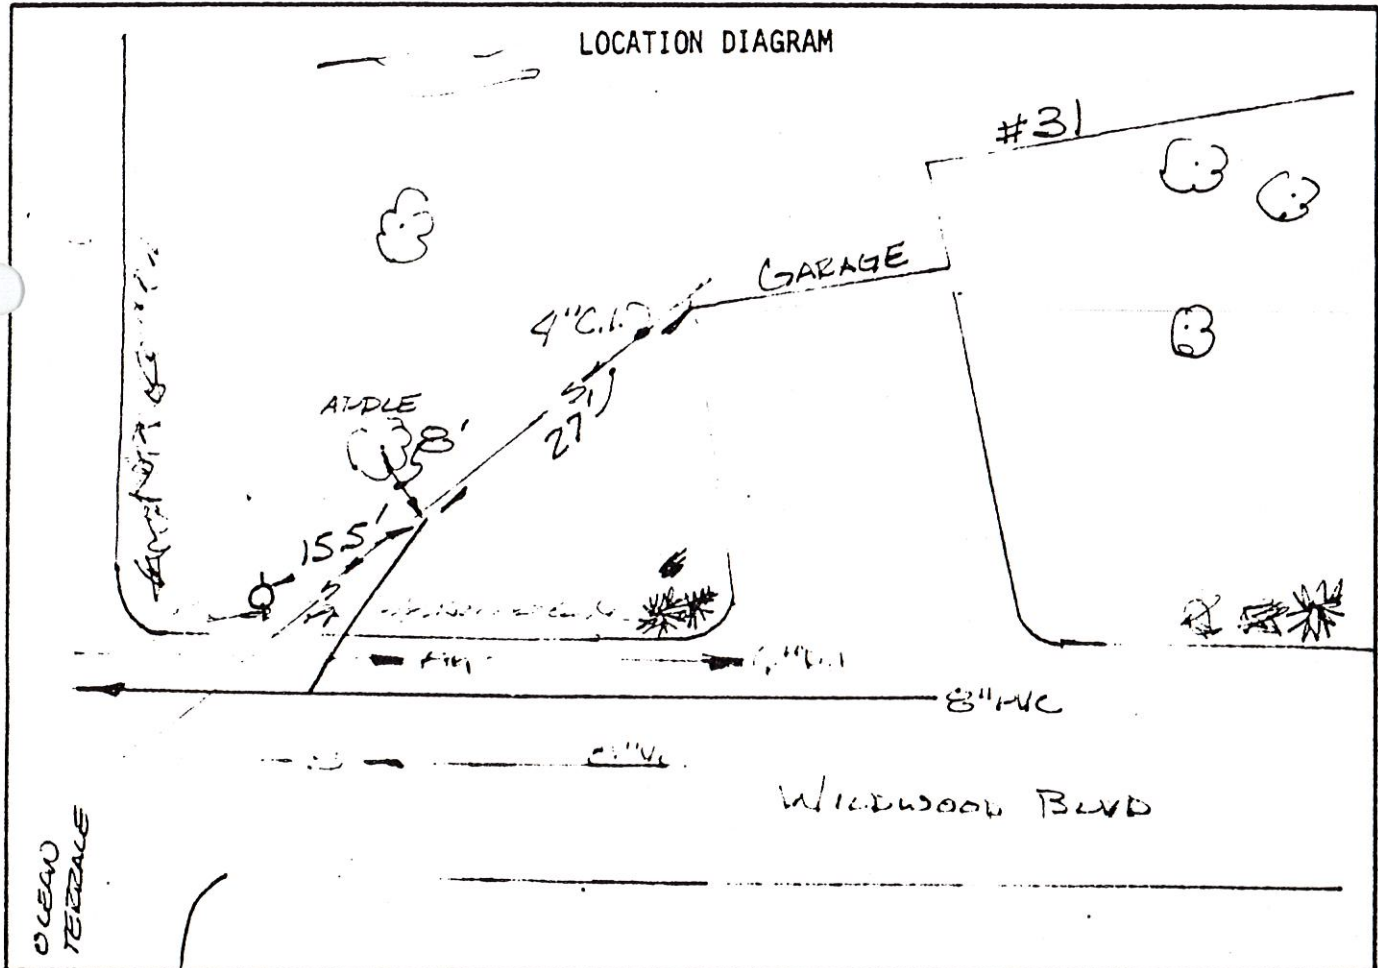

Remarks: ROCK RUSH TO BE REMOVED ON CONNECTION
N.E. 6\"/>

SAMPLE BUILDING SEWER SKETCH

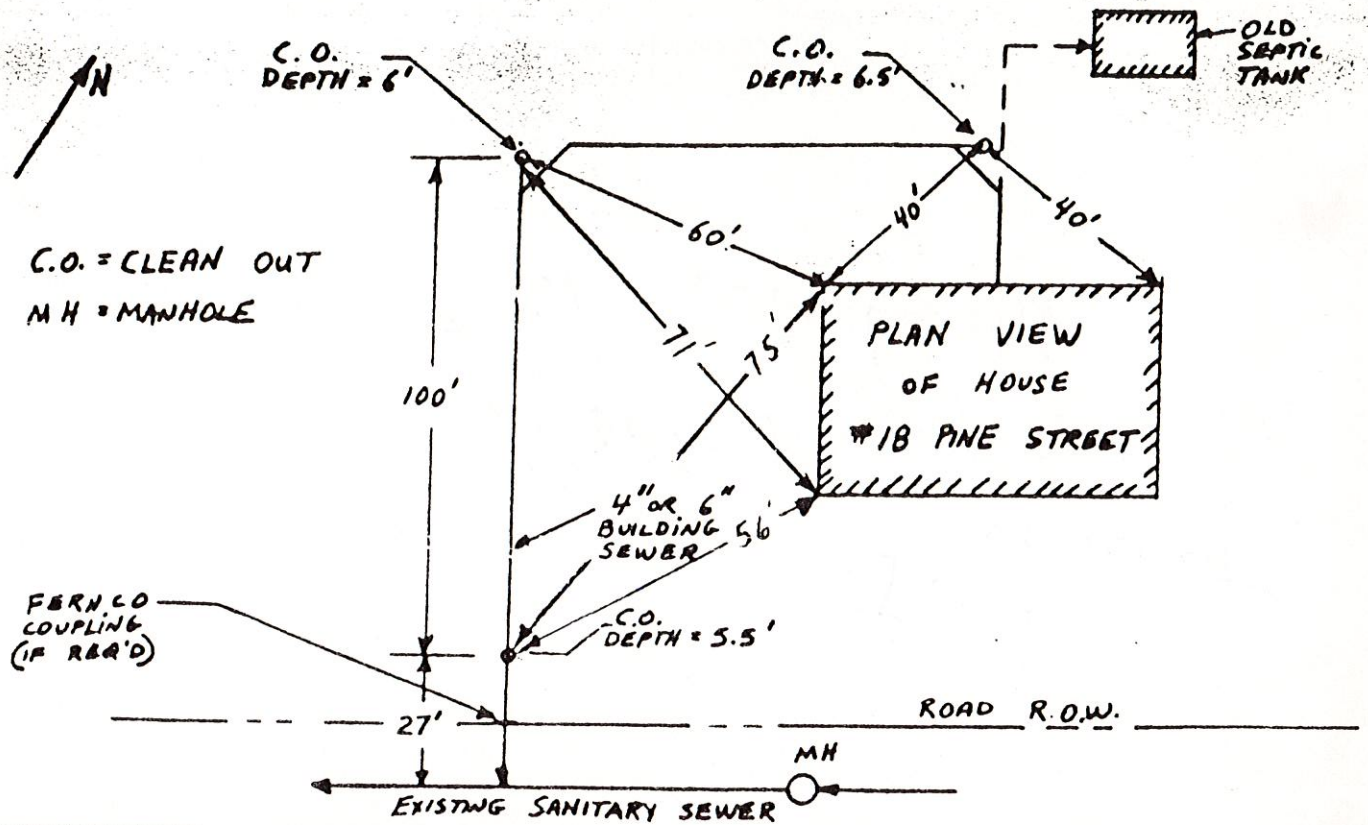


NAME: Gordon Morton

ADDRESS: 31 Wildwood

CONTRACTOR: Scott Dugan

DATE: 6-14-84

COLLECTOR OR INTERCEPT

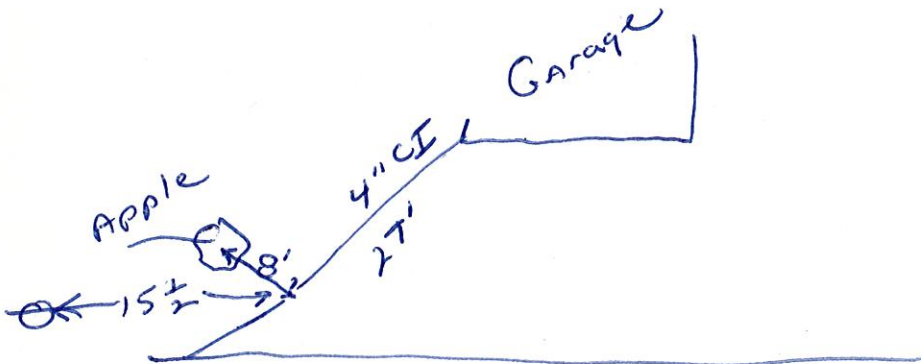

SANITARY SEWER SERVICE LOCATION

Town, City of: CUMBERLAND

Date Installed 7/25/83

Street WILLOWOOD BLVD

Type, Size of Service Pipe 6" PVC

Dwelling No. 32

Connection at Sewer Main 8" 6" C.I. SADDLE

Occupant _____


Depth, End of Service Pipe 2.5' @ EXISTING SEWER

Owner _____

Length of Service Pipe Laid 36.5'


Measured, Located By _____

Project Contractor S.E. MACMILLAN

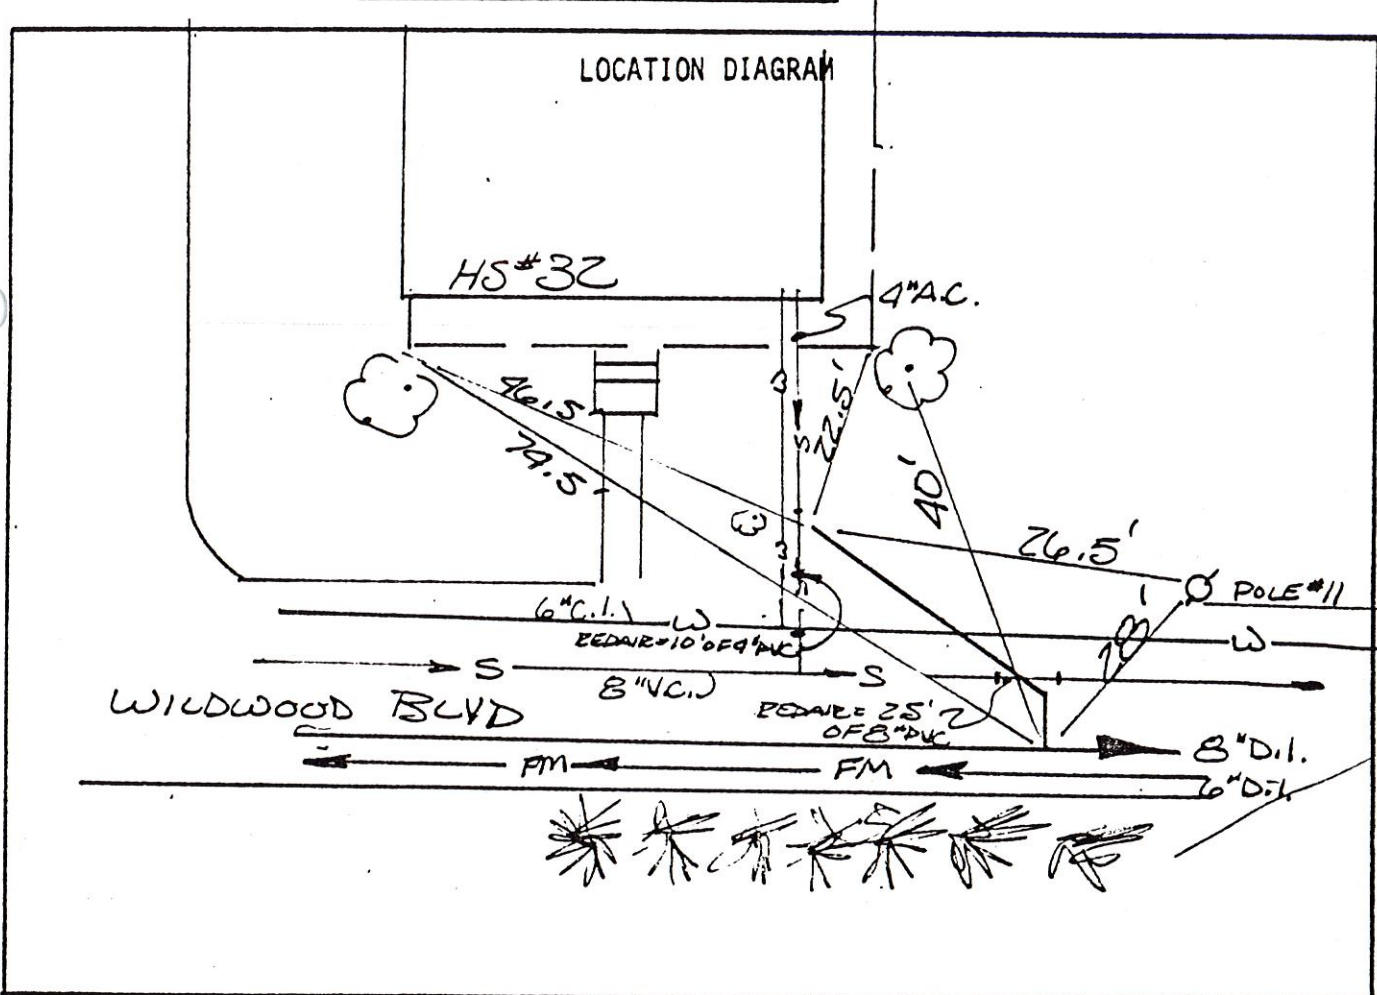

Remarks: 6" PVC GOES UNDER 8" V.C. SEWER BY 2' ± & UNDER
6" WATER MAIN BY 3" - NEED 6" x 9" REDUCER & 220 BEAM TO
CONNECT SEWERS

SAMPLE BUILDING SEWER SKETCH

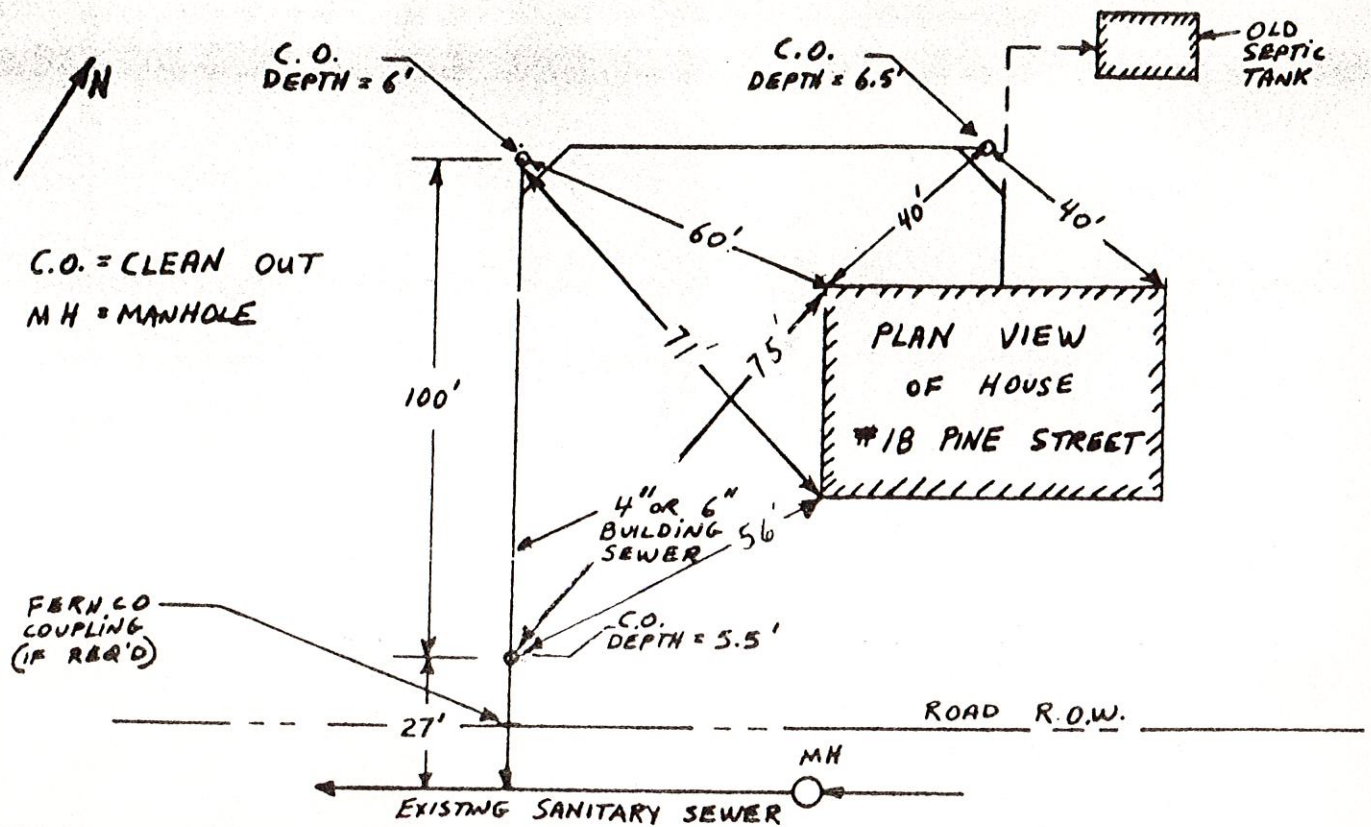

NAME: Loyd Helmsaw
 ADDRESS: 32 Wildwood
 CONTRACTOR: Scott Ovgas

DATE: 6-15-84
 COLLECTOR OR INTERCEPT

